

MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

31st-JULY-2018

PACKAGE-II	STATUS AS ON 31/07/2018
Up to Last Month Block D03	<ul style="list-style-type: none"> • Overhead water tank Base slab and Wall Reinforcement completed. • Terrace projection casted of length 12mtrs. • Terrace parapet brick work of wings-1 & 4 completed. • 20% Plaster done at 14th floor lvl. • Chicken wire mesh fixing on external wall in progress for external Plaster. • 100% Cpvc Piping done at 14th floor lvl. • CI piping work done up to 12th floor lvl. • POP cornice done up to 12th floor lvl. • Water proofing in Toilets completed from 1st to 3rd floor lvl. • Balance 70% wall conduiting and GI boxes completed at 13th floor lvl. (Total 100%).
Current Month Activity	<ul style="list-style-type: none"> • Overhead water tank Base slab casted. • Terrace projection slab 20% casted.(Total 40%) • Terrace parapet brick work 45% completed.(Total 90%) • Balance 80% Plaster done at 14th floor lvl. (Total 100 %). • External Plaster wing-4 100% completed. • 100% Cpvc Piping done at 14th floor lvl. • 90% CI piping work done at 13th floor lvl. • 25% CI piping work done at 14th floor lvl. • GI piping in Toilets done up to 6th floor lvl. • 100% Water proofing in Toilets completed at 4th & 5th floors. • 100% wall conduiting and GI boxes completed at 14th floor lvl.
Up to Last Month Block D04	<ul style="list-style-type: none"> • Mumnty slab casted. • Machine Room columns 10nos casted. • Brick work at 14th floor lvl in progress. • 100% plaster done at 8th floor lvl. • 70% plaster completed at 9th floor lvl. • 100% door frames fixed at 9th & 10th floor lvl. • 100% cPVC piping done at 11th & 12th floor lvl. • POP cornice up to 3rd floor completed. • 100% wall conduiting and G.I boxes fixing completed at 8th floor lvl.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Machine Room columns 100% casted. • 20% Brick work done at 14th floor lvl. • 100% plaster done at 8th floor lvl. • Balance 30% plaster completed at 9th floor lvl. • 100% door frames fixed at 11th floor lvl and 80% at 12th floor lvl completed. • 90% cPVC piping done at 13th floor lvl. • POP cornice from 4th to 9th floor lvl completed. • 100% wall conduiting and G.I boxes fixing completed at 9th & 10th floor lvl and 20% at 11th floor lvl.
Up to Last Month Block D05	<ul style="list-style-type: none"> • 14th floor Roof slab 50% casted. • 50% Brick work completed at 13th floor lvl. • 100% door frames fixed at 8th & 9th floor lvl. • 100% plaster completed at 2nd & 3rd floor lvl. • Balance 50% plaster completed at 6th floor lvl. • 100% plaster done at 7th & 8th floor lvl. • 100% cPVC piping completed at 10th & 11th floor lvl. • CI work done from 2nd to 6th floor lvl. • 100% wall conduiting and G.I boxes fixing done at 7th & 8th floor lvl.
Current Month Activity	<ul style="list-style-type: none"> • Balance 50% 14th floor Roof slab casted. (Total 100%). • Mumnty columns 100% casted. • Mumnty slab shuttering work in progress. • Balance 50% Brick work completed at 13th floor lvl. (Total 100%). • 100% door frames fixed at 10th & 11th floor lvl and 80% at 12th floor lvl. • 100% plaster completed at 9th floor lvl. • 40% plaster done at 10th floor lvl. • 100% cPVC piping completed at 12th & 13th floor lvl. • 100% wall conduiting and G.I boxes fixing done at 9th & 10th floor lvl and at 11th floor lvl 20% completed.
Up to Last Month Block D06	<ul style="list-style-type: none"> • 100% columns casted at 14th floor lvl. • 14th floor shuttering for two flats in progress. • 90% Brick work done from 7th to 10th floor lvl. • 15% Basement ceiling plaster completed. (Total 95%). • 10nos Basement columns plaster completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% columns casted at 14th floor lvl. • 14th floor Roof slab Reinforcement binding for two flats in progress. • 90% Brick work done at 11th & 12th floor lvl. • 100% wall conduiting and G.I boxes fixing done up to 4th floor lvl. • 42 Nos Basement columns plaster completed.
Up to Last Month Block D07	<ul style="list-style-type: none"> • 80% Basement columns plaster completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	
Up to Last Month Block D08	<ul style="list-style-type: none"> • 80% Basement Ceiling plaster completed. • 80% Basement columns plaster completed.
Current Month Activity	
Up to Last Month Non Tower	<ul style="list-style-type: none"> • 650 Sqm PCC completed. (Total 12800 Sqm / 15886 Sqm). • 750 Sqm Stitch slab casted. (Total 12750 Sqm/ 15886Sqm) • Basement Slab 530 Sqm casted. (Total 4380 Sqm). • 20 nos. Pile caps casted. (Total 213nos).
Current Month Activity	<ul style="list-style-type: none"> • 760 Sqm PCC completed. (Total 13560 Sqm / 15886 Sqm). • 100 Sqm Stitch slab casted. (Total 12850 Sqm/ 15886Sqm) • Basement Slab 643 Sqm casted. (Total 5023 Sqm). • 8nos Pile caps casted. (Total 221nos). • Basement columns 27 Nos casted. (Total 201).
Up to Last Month Retaining Wall	<ul style="list-style-type: none"> • Retaining wall-2 of length 18mtrs casted in 1st lift. (Total 92 mtrs casted.) • Water proofing with Kota stone on Retaining wall-1 & 2 in Progress.
Current Month Activity	<ul style="list-style-type: none"> • Retaining wall-2 of length 28mtrs 2nd lift casted. • Retaining wall shuttering of 2nd lift in Progress.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-II on 31st-JULY-2018

In Block D-03 Outer Plastering in Progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**In Block D-04 Machine Room columns 100% casted.
Terrace parapet wall Brick work in progress.**



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**In Block D-05 Terrace Roof slab 100% casted.
Mumnty slab shuttering work in progress.**



Progress Report No. 27 (1st JULY- 18 – 31st JULY- 18)



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block D-06 Terrace slab Reinforcement binding of two flats in progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

PACKAGE-III	STATUS AS ON 31/07/2018
Up to Last Month Block C01	<ul style="list-style-type: none"> • Level 00: Remaining 30% column completed. • Level 01: 100% slab completed, 50% column completed.
Current Month Activity	<ul style="list-style-type: none"> • Level 01: Remaining 50% column completed. • Level 02: 100% slab completed, 100% column completed. • Level 03: 50% slab completed, Remaining 50% shuttering & reinforcement work is on progress.
Up to Last Month Block C02	<ul style="list-style-type: none"> • Level 02: Remaining 50% Slab completed, 100% column completed. • Level 03: 100% slab completed, 50% column completed, shuttering is on progress.
Current Month Activity	<ul style="list-style-type: none"> • Level 03: Remaining 50% column completed. • Level 04: 100% slab completed & 100% column completed. • Level 05: 50% slab completed & shuttering is on progress. • Level 01: 50% brick work completed.
Up to Last Month Block C06	<ul style="list-style-type: none"> • Level 06: 100% slab completed, 100% column completed. • Level 07: 50% slab completed. • Level 01: Brick work completed. • Level 02: Brick work completed.
Current Month Activity	<ul style="list-style-type: none"> • Level 07: Remaining 50% slab completed, 100% column completed. • Level 08: 100% slab completed, 25% column completed. • Level 03: Brick work completed, Door frame completed, electrical wall conduiting completed. • Level 01: 50% plaster completed. • Level 01&02: Kitchen counter completed.
Up to Last Month Block C07	<ul style="list-style-type: none"> • Level 04: Remaining 70% column casted. • Level 05: 100% slab completed, 50% column casted. • Level 01: Brick work completed. • Level 02: Brick work completed.
Current Month Activity	<ul style="list-style-type: none"> • Level 05: Remaining 50% column casted. • Level 06: 100% slab completed, 100% column completed. • Level 07: slab shuttering 50% completed. • Level 03: Brick work completed. • Level 01&02: Door frame completed, electrical wall conduiting completed, kitchen counter completed. • Level 01: Plaster work completed.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month Block C08	<ul style="list-style-type: none"> • Level 07: Remaining 50% column completed. • Level 08: 100% slab completed, 100% column completed. • Level 04: Remaining 85% brickwork completed. • Level 05: Brickwork completed. • Level 06: Brickwork completed. • Level 07: Brick work in progress. • Level 02: Remaining 35% plaster completed. • Level 03: Plaster completed. • Level 04: Plaster completed.
Current Month Activity	<ul style="list-style-type: none"> • Level 09: 100% slab completed, 80% column completed. • Level 10: 50% slab shuttering completed. • Level 07: Brick work 50% completed. • Level 05&06: Door frame completed, electrical wall conduiting completed, Kitchen counter completed. • Level 05&06: Plaster completed.
Up to Last Month Block C09	<ul style="list-style-type: none"> • 3 nos. pile casted.
Current Month Activity	<ul style="list-style-type: none"> • 142 nos. pile casted.(145/195)
Up to Last Month Block C11	<ul style="list-style-type: none"> • 59 piles casted this month. (Total 195/195).
Current Month Activity	<ul style="list-style-type: none"> • 75% P.C.C completed, pile cap reinforcement is on progress.
Up to Last Month Block C12	<ul style="list-style-type: none"> • Level 00: 100% slab completed, 100% column completed.
Current Month Activity	<ul style="list-style-type: none"> • Level 01: 100% slab completed, 100% column completed. • Level 02: 100% slab completed, 50% column completed & slab 40% shuttering is on progress.
Up to Last Month UG Tank	<ul style="list-style-type: none"> • Domestic tank 2nos, Row water tank 2 no's, Fire tank 2nos& pump room base slab completed. • Pump room wall reinforcement work is in progress.
Current Month Activity	<ul style="list-style-type: none"> • U.G Tank wall reinforcement work is in progress.
Up to Last Month Non Tower	<ul style="list-style-type: none"> • 57 1st lift & 105 2nd lift mtr retaining wall completed. • 50.72% PCC done. • 45.76 % stitch slab casted. • 44.11% circular column casted. • 2250/18730 sqm basement non tower slab casted • Pile casted (602/774) nos.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	Month
	<ul style="list-style-type: none">• 2.66% PCC done. (Total 53.38% done).• 1.78 % stitch slab casted. (Total 47.54% done).• 7.0% circular column casted. (Total 51.11% done).• Pile casted 09 nos. (665/774).• 68 sqm basement non tower slab casted (3287/18730)

PHOTOGRAPHS OF PACKAGE-III on 31Th JULY-2018

In Block C-02 level-05 slab shuttering is in progress.
In Block C-01 level -03 slab shuttering is on progress.
In Block C-12 level -02 slab shuttering work is on progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**Non Tower Slab shuttering in progress.
In Block C-08 level-10 shuttering & Reinforcement bonding in progress.**



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block C-11 Pile caps & Stitch slab Reinforcement binding in progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

PACKAGE-IV	STATUS AS ON 31/07/2018
Block A01 UpTo Last Month	<ul style="list-style-type: none"> • 50% Remaining Twelfth Floor slab casting work completed. • 100% Thirteen Floor slab casting work completed. • Ninth floor brick work in progress. • Seventh floor Door Frame fixing work in progress. • Seventh floor internal Electrical wall conduit work completed. • Sixth floor plaster work in progress. • Eight floor internal water supply work completed. • Fifth floor toilet sunken water proofing work completed.
Current Month Activity	<ul style="list-style-type: none"> • 50% Terrace Floor slab shuttering and steel binding work in progress. • 80% Tenth floor brick work completed. • Eight & Ninth floor Door Frame fixing work completed. • Eight & Ninth floor internal Electrical wall conduit work completed. • 80% Ninth floor plaster work completed. • Eighth floor internal water supply work completed. • Ninth floor SCI work completed. • Sixth floor toilet sunken water proofing work completed. • 50% First floor POP Cornices work completed.
Block B04 UpTo Last Month	<ul style="list-style-type: none"> • 100% Eleventh to Twelfth Floor columns casting work completed. • 50% Twelfth Floor slab casting work completed. • Tenth Floor brick work in progress. • Seventh & Eight floor Plaster work completed. • Ninth floor Door Frame fixing work completed. • Eight & Ninth floor internal water supply work completed. • Eight floor internal Electrical wall conduit work completed. • Eight floor toilet sunken water proofing work completed.
Current Month Activity	<ul style="list-style-type: none"> • Remaining 50% Twelfth Floor slab casting work completed. • 100% Twelfth to Thirteen Floor columns casting work completed. • 50% Thirteen Floor slab casting work completed & Remaining 50% shuttering work in progress. • 50% Eleventh Floor brick work completed. • 40% Tenth Floor Plaster work completed. • Tenth floor Door Frame fixing work completed. • Tenth floor internal water supply work completed. • Ninth floor SCI work completed. • Ninth & Tenth floor internal Electrical wall conduit work completed. • 50% Eighth floor POP Cornices work completed. • Seventh floor toilet sunken water proofing work completed



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Block B05 UpTo Last Month	<ul style="list-style-type: none"> • 100% thirteen floor slab casting work completed. • 100% Eleventh floor brick work completed. • 100% Tenth floor plastering work completed. • Tenth floor door frame fixing work completed. • Tenth floor internal water supply work completed. • Tenth floor Electrical internal wall conducting work completed. • Fourth floor toilet sunken water proofing work in progress.
Current Month Activity	<ul style="list-style-type: none"> • 50% thirteen to Terrace floor columns casting work completed. • 100% Eleventh floor plastering work completed. • Eleventh floor door frame fixing work completed. • 50% Eleventh floor internal water supply work completed. • 50% Eleventh floor SCI work completed. • Eleventh floor Electrical internal wall conducting work completed. • Ninth floor toilet sunken water proofing work completed.
Block C13 UpTo Last Month	<ul style="list-style-type: none"> • 100% columns casting above Terrace floor. • Twelfth floor brick work completed. • Parapet wall brick work completed. • Twelfth floor staircase plaster work completed. • Eight floor toilet sunken water proofing work completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% Mumty Slab casting work completed. • Up to Tenth Floor common area & Ceiling putty one code completed. • Up to Tenth Floor POP Cornice work completed. • Ninth floor toilet sunken water proofing work completed.
Block C14 UpTo Last Month	<ul style="list-style-type: none"> • 100% Columns casting completed for mumty machine room. • Twelfth floor plaster work completed. • Twelfth floor SCI work completed. • Eleventh floor staircase plaster work completed. • Eleventh floor toilet sunken water proofing work in progress. • 70% External plaster work completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% Machine room and water tank base slab casting completed. • Machine room columns casting work in progress. • 100% Projection casting work completed. • 100% External plaster work completed up to terrace level. • Twelfth floor toilet sunken water proofing work completed.
Block C03 UpTo Last Month	<ul style="list-style-type: none"> • 100% columns casting Seventh to Eight floor completed. • 100% Eight floor slab casting work completed. • Fourth floor brick work in progress. • Second floor internal water supply work in progress.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • 100% columns casting Eight to Ninth floor completed. • 100% Ninth floor slab casting work completed. • 100% columns casting Ninth to Tenth floor completed. • 100% Tenth floor slab casting work completed. • Columns casting Tenth to Eleventh floor in progress. • Fifth floor brick work completed. • 50% First floor internal wall electrical conduiting work completed. • 50% First floor door frame fixing work completed. • Third floor internal water supply work completed. • Third floor SCI work completed.
Block C04 UpTo Last Month	<ul style="list-style-type: none"> • 100% Fourth floor slab casting work completed. • 100% Columns casting Fourth to Fifth Floor completed. • 100% Fifth floor slab casting work completed. • Second floor brick work completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% Columns casting Fifth to Sixth Floor completed. • 100% Sixth floor slab casting work completed. • 100% Columns casting Sixth to Seventh Floor completed. • 100% Seventh floor slab casting work completed. • 80% Third floor brick work completed. • Second floor internal water supply work in progress.
Block C05 UpTo Last Month	<ul style="list-style-type: none"> • 100% columns casting Second to Third floor completed. • 100% Third floor slab casting work completed. • 100% columns casting Third to Fourth floor completed. • 100% Fourth floor slab casting work completed. • 50% First floor brick work completed.
Current Month Activity	<ul style="list-style-type: none"> • 100% columns casting Fourth to Fifth floor completed. • 100% Fifth floor slab casting work completed. • 100% columns casting Fifth to Sixth floor completed. • 100% Sixth floor slab casting work completed. • 100% Sixth to Seventh floor columns casting work completed. • Seventh floor slab shuttering and steel binding in progress. • 50% Third floor brick work completed.
Non Tower UpTo Last Month	<ul style="list-style-type: none"> • 350 sqm NTA slab casting work completed. • 450 Sqm Stitck slab casting completed. (14200sqm/15800 sqm) • 297 mtrs out of 314 mtr Retaining wall casting work completed. • 280 mtrs out of 314 mtr Kota stone water proofing work completed. • Basement round columns casting work in progress. • 30% STP Foundation casting work completed.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • 600 sqm NTA slab casting work completed. (8200sqm/15900sqm) • 297 mtrs out of 314 mtr Retaining wall casting work completed. • 280 mtrs out of 314 mtr Kota stone water proofing work completed. • Basement round columns casting work in progress. • 100% STP Foundation casting work completed. • 20% STP RCC wall casting work completed. • RCC Drain work in progress.
Sample Flat Type A,B & C Status	<ul style="list-style-type: none"> • Painting work of walls & Ceiling completed. • Tile fixing work completed. • Internal Electrical work completed. • Water supply & Drainage work completed.

PHOTOGRAPHS OF PACKAGE-IV on 31st JULY -2018

**IN BLOCK C03- ELEVENTH FLOOR SLAB SHUTTERING WORK IN PROGRESS.
IN BLOCK C04- SEVENTH FLOOR SLAB CASTING WORK COMPLETED.
IN BLOCK C05- SIXTH FLOOR SLAB CASTING WORK COMPLETED.**



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**IN BLOCK C14-MACHINE ROOM COLUMNS CASTING IN PROGRESS.
IN BLOCK C13- MUMTY MACHINE ROOM BASE SLAB CASTING WORK
COMPLETED.**



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

**IN BLOCK C-14 OUTER PLASTER WORK COMPLETED.
IN BLOCK A-01 TERRACE FLOOR SHUTTERING WORK IN PROGRESS.
IN BLOCK B-04 THIRTEEN FLOOR SLAB WORK COMPLETED.**



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

IN BLOCK B04- THIRTEEN FLOOR SLAB CASTING WORK IN PROGRESS.

IN BLOCK B05- THIRTEEN FLOOR SLAB CASTING WORK COMPLETED.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

IN BLOCK C13- PROJECCION SLAB CASTING WORK IN PROGRESS.



Progress Report No. 27 (1st JULY- 18 – 31st JULY- 18)



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

PACKAGE-V	STATUS AS ON 31/07/2018
<p>Up to Last Month</p> <p>Block B01</p>	<ul style="list-style-type: none"> • Machine Room columns casted. • Terrace Projection 50% casted. • Terrace parapet wall 80% casted. • Brick work at 12th floor lvl completed. • Plaster 50% done at 12th floor lvl. • Water proofing in toilet sunken area at 10th & 11th floor lvl in progress. • Wall putty work is completed at 4th floor. • External plaster 45% completed.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Water tank base slab shuttering & reinforcement binding work is in progress. • Terrace Projection 20% casted.(Total 70%). • Terrace parapet slab 20% casted.(Total 100%). • POP cornice work done up to 11th floor. • Water proofing in toilet sunken area at 12th floor completed. • External plaster 20% completed.(Total 65%). • Kitchen wall tiling fixing work completed at 1st floor lvl. • C.I vertical pipe fixing completed up to 11th floor.
<p>Up to Last Month</p> <p>Block B02</p>	<ul style="list-style-type: none"> • Mumnty slab casted. • Terrace parapet slab 50% casted. • Mumnty Brickwork 50% completed. • Water tank Base slab Reinforcement binding in progress. • Plaster work at 13th floor lvl completed. • Electrical wall conduiting & GI boxes fixing done up to 13th floor lvl. • Water proofing in toilet sunken area done at 8th, 9th & 10th floor lvl. • POP cornice completed at 11th & 12th floor lvl.
<p>Current Month Activity</p>	<ul style="list-style-type: none"> • Water tank base slab casted. • Terrace parapet slab 40% casted. (Total 90%). • Terrace projection slab 25 meters casted. • Mumnty Brickwork 90% completed. • Staircase no 1 plaster work is progress. • Water proofing in toilet sunken area done at 11th, 12th and 13th floor lvl. • External plaster of wing-1 is in progress. • Kitchen wall tiling fixing work done at 1st & 2nd floor lvl. • C.I vertical pipe fixing completed up to 13th floor.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Up to Last Month	<ul style="list-style-type: none"> • 100% columns casted at Stilt flr lvl.
Block B03	
Current Month Activity	
Up to Last Month Block C15	<ul style="list-style-type: none"> • Mumnty roof slab casted. • Water tank base slab casted. • Water tank wall reinforcement work is in progress. • Machine room column 90% casted. • Mumnty Brickwork 60% completed. • Balance 50% Brick work done at 11th floor lvl. • Plaster work at 8th floor completed. • Plaster work at 9th floor lvl in progress. • Electrical wall conduiting & GI boxes fixing done at 10th floor lvl. • 90% cPVC piping work done in 10th floor lvl. • 90% CI piping work done at 7th floor lvl. • Water proofing of Toilets sunken area done at 6th & 7th floor lvl.
Current Month Activity	<ul style="list-style-type: none"> • Terrace to Mumnty staircase shuttering & reinforcement work is in progress. • Mumnty Brickwork 30% completed. (Total 90%). • Terrace projection slab 30 meters casted. • Terrace parapet slab 100% casted. • Plaster work at 9th floor lvl in progress. • Electrical wall conduiting & GI boxes fixing done at 11th floor lvl. • 90% cPVC piping work done in 11th floor lvl. • 90% CI piping work done at 8th floor lvl. • Water proofing of Toilets sunken area done at 8th & 9th floor lvl.
Up to Last Month Block C16	<ul style="list-style-type: none"> • Water tank Base slab casted and Wall Reinforcement binding in progress. • Mumnty Brickwork 70% completed. • Terrace parapet slab 100% casted. • Terrace elevation projection 65% casted. • Plaster work is completed at 8th floor lvl while 9th floor lvl 80% done. • Electrical DB & ONT box fixing work in progress at 8th floor lvl. • Balance 75% Door frames fixed in 9th floor lvl. • Water proofing in Toilets done at 7th floor lvl and 8th floor lvl is on progress. • GI piping completed up to 8th floor lvl.



MONTHLY PROGRESS REPORT

CGEWHO – GREATER NOIDA PROJECT

Current Month Activity	<ul style="list-style-type: none"> • Water tank Wall shuttering work is in progress. • Mumty Brickwork 20% completed. (Total 90%). • Terrace projection slab 35% casted. (Total 100%). • 100% Plaster work is completed at 9th floor lvl. • Electrical DB & ONT box fixing work in progress at 9th floor lvl. • Water proofing in Toilets done at 9th floor lvl. • Waterproofing in balcony & kitchen sunken done up to 9th floor. • External plaster 30% completed. • Kitchen wall tiling fixing done up to 3rd floor lvl.
Up to Last Month Non Tower	<ul style="list-style-type: none"> • 500 Sqm Basement Roof slab casted. (Total 8907 Sqm Casted). • 10% Basement ceiling plaster done. • Basement drain excavation, dressing levelling and PCC 70% completed. • Basement drain reinforcement in progress. • Basement drain 80 metres base slab casted.
Current Month Activity	<ul style="list-style-type: none"> • 290 Sqm Basement Roof slab casted. (Total 8617 Sqm Casted). • 5% Basement ceiling plaster done. • Basement drain casting 65% completed. • Basement PCC 10% done.
Up to Last Month Retaining Wall	<ul style="list-style-type: none"> • Water proofing (Kota stone) on outer side of Retaining wall 98% completed.
Current Month Activity	<ul style="list-style-type: none"> • Water proofing (Kota stone) on outer side of Retaining wall 100% completed.
Up to Last Month Boundary Wall	<ul style="list-style-type: none"> • Boundary wall excavation, footing 95 % completed. • Plinth Beam below GL of length 120 mtrs casted. • Plinth beam at 150mm lvl of length 200mtrs casted. • Brick work above plinth beam 150mtrs done
Current Month Activity	<ul style="list-style-type: none"> • Plinth Beam at NGL 98% completed. • Plinth beam at +150 mm lvl 98% completed. • Brick work above plinth beam 90% completed.



**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

PHOTOGRAPHS OF PACKAGE-V on 31st JULY-2018

In Block C-16 Outer Plastering work in Progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block B-01 outer Plastering work is in progress.




MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block B-02 Over head water tank Reinforcement binding work is in progress.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

In Block C-15 Over head water tank wall Reinforcement binding in progress.

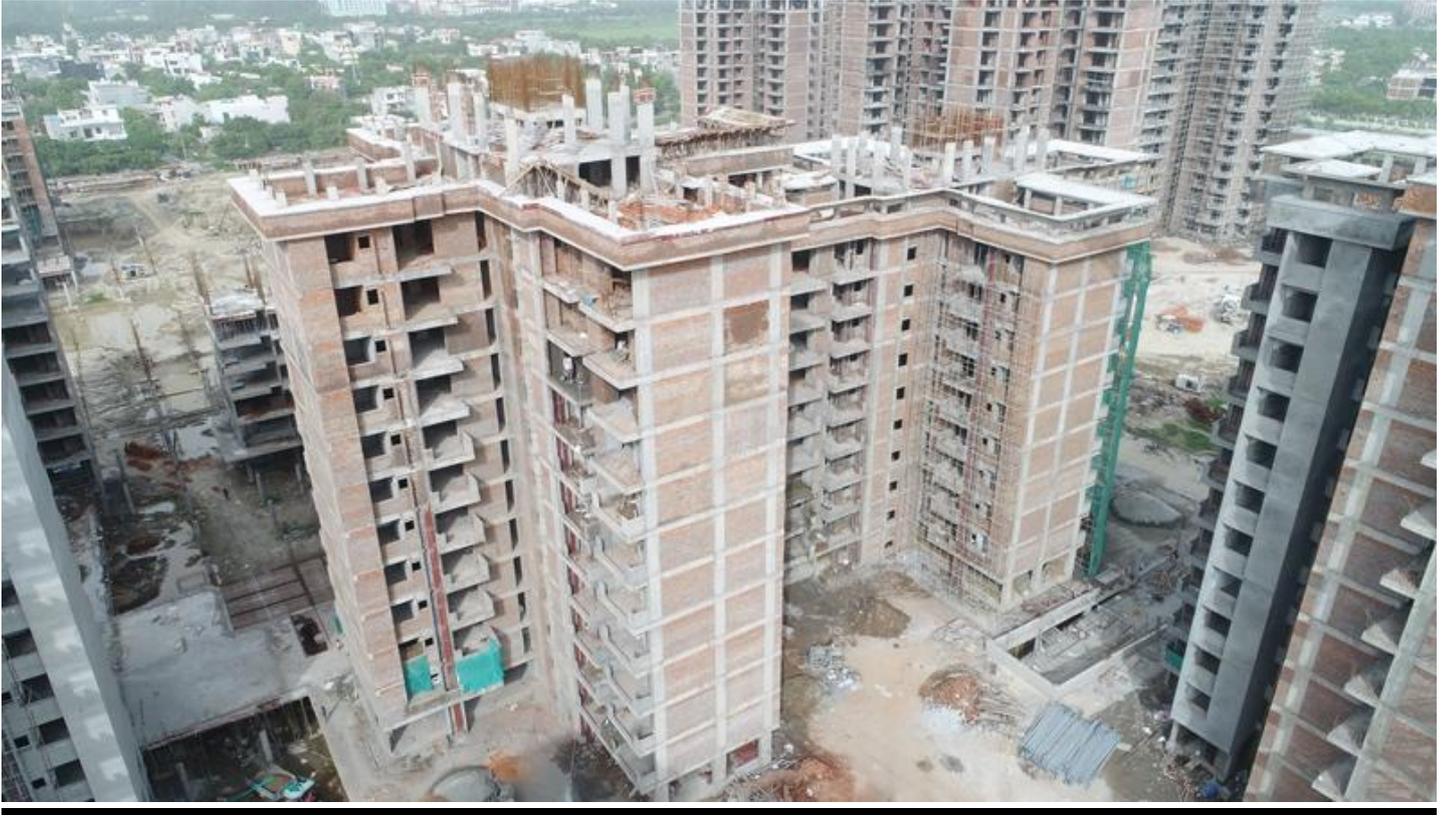

**MONTHLY PROGRESS REPORT
CGEWHO – GREATER NOIDA PROJECT**

QUALITY CONTROL

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS
CONDUCTED AT SITE:**

S. No.	Materials	Source From	Test Date	Tests done	Result
1	Coarse Sand	Bajpur		Each truck	Sieve Analysis & Silt content
2	Coarse Aggregate	Nangal		Each truck	Sieve Analysis & Impact Value
3	Fine Sand	Yamuna Nagar		Each truck	Sieve Analysis & Silt content
4	Bricks	Greater Noida		Each truck	Dimension, Water Absorption & Compressive strength
5	Cement	Third party testing is being done			
6	Steel	Third party testing is being done			
7	Piles Integrity	Third party testing is being done			
8	Soil Compaction	Third party testing is being done			
9	STP water	Third party testing is being done			
10	RCC Cubes are being tested and Register is being maintained.				
11	Slump test conducted at site to insure workability if concrete.				



PHOTOGRAPH OF QUALITY CONTROL AT SITE

Fine Aggregate Sieve Analysis Testing



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Slump test of Concrete.



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

Cube Testing Of Concrete



MONTHLY PROGRESS REPORT CGEWHO – GREATER NOIDA PROJECT

20 & 10mmAggregate Sieve Analysis Testing.

