

**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**CGEWHO – CHENNAI PHASE-III  
PROJECT**



**PROGRESS REPORT**

**STATUS AS ON : 31.07.2022**



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

31.07.2022

BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> JULY -2022
A1 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth Floor level slab-R.C.C 100% completed.</li> <li>▪ Fourth floor Columns Concrete 100% completed.</li> <li>▪ Fifth Floor level slab –1<sup>st</sup> Half R.C.C 100% completed.</li> <li>▪ Fifth floor Columns Concrete 50% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Barbending works for 2<sup>nd</sup> half of Fifth floor level slab 75% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Second floor 95% completed.</li> <li>▪ Third floor 50% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 50% completed.</li> <li>▪ First floor 45% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 10% completed.</li> </ul> </li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 85% completed.</li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Fifth Floor level slab-R.C.C 100% completed.</li> <li>▪ Fifth floor Columns Concrete 60% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 1<sup>st</sup> half of Sixth floor level slab 15% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Second floor 95% completed.</li> <li>▪ Third floor 70% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 50% completed.</li> <li>▪ First floor 90% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 20% completed.</li> </ul> </li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 90% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
A2 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor level slab – R.C.C 100% completed.</li> <li>▪ Fourth floor Columns Concrete 50% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 1<sup>st</sup> half of Fifth floor level slab 25% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 90% completed</li> <li>▪ Third floor 10% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 65% completed.</li> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 10% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor level slab – R.C.C 100% completed.</li> <li>▪ Fourth floor Columns Concrete 60% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering and barbending works for 1<sup>st</sup> half of Fifth floor level slab 70% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 60% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 65% completed.</li> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 15% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 15% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> JULY -2022
B1 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab-R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 100% completed.</li> </ul> </li> </ul> </li>   <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor 95% completed.</li> <li>▪ Fifth floor 90% completed.</li> <li>▪ Sixth floor 90% completed.</li> <li>▪ Seventh floor 85% completed.</li> <li>▪ Eighth floor 85% completed.</li> <li>▪ Ninth floor 85% completed.</li> <li>▪ Tenth floor 75% completed.</li> <li>▪ Terrace floor Parapet wall 50% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 80% completed.</li> <li>▪ First floor to Fifth floor 90% completed.</li> <li>▪ Sixth floor 75% completed.</li> <li>▪ Seventh floor 60% completed.</li> <li>▪ Eighth floor 35% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor to Fifth floor 90% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab-R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 100% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for Lift Head room Slab 65% completed and balance works on progress.</li> </ul> </li> </ul> </li>   <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor 95% completed.</li> <li>▪ Fifth floor 90% completed</li> <li>▪ Sixth floor 90% completed</li> <li>▪ Seventh floor 90% completed.</li> <li>▪ Eighth floor 85% completed</li> <li>▪ Ninth floor 85% completed.</li> <li>▪ Tenth floor 75% completed.</li> <li>▪ Terrace floor Parapet wall 50% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 80% completed.</li> <li>▪ First floor to Fifth floor 90% completed.</li> <li>▪ Sixth floor 75% completed.</li> <li>▪ Seventh floor 60% completed.</li> <li>▪ Eighth floor 50% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor to Fifth floor 90% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Sixth floor 50% completed.</li> <li>• <b>External Finishing Works</b> <ul style="list-style-type: none"> <li>◆ <b>External Plastering</b> <ul style="list-style-type: none"> <li>▪ In South Side Elevation 60% completed.</li> </ul> </li> </ul> </li> <li>• <b>Model Flat</b> Finishing works 90% completed.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Sixth floor 50% completed.</li> <li>◆ <b>Fixing of Balcony Rails</b> <ul style="list-style-type: none"> <li>▪ Balcony railing work 10% completed.</li> </ul> </li> <li>• <b>External Finishing Works</b> <ul style="list-style-type: none"> <li>◆ <b>External Plastering</b> <ul style="list-style-type: none"> <li>▪ In South Side Elevation 100% completed.</li> <li>▪ In East Side Elevation 10% completed.</li> </ul> </li> </ul> </li> <li>• <b>Model Flat</b> Finishing works 90% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
B2 BLOCK	<ul style="list-style-type: none"> <li>• <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Third floor level slab – R.C.C 100% completed.</li> <li>▪ Third floor Columns Concrete 80% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 1<sup>st</sup> half of Fourth floor level slab 15% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>• <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 50% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>• <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Third floor level slab – R.C.C 100% completed.</li> <li>▪ Third floor Columns Concrete 80% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 1<sup>st</sup> half of Fourth floor level slab 15% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>• <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 50% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
C1 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab – R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 90% completed.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Seventh floor 95% completed.</li> <li>▪ Eighth floor 90% completed.</li> <li>▪ Ninth floor 90% completed.</li> <li>▪ Tenth floor 40% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 85% completed.</li> <li>▪ First floor to Third floor 95% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 90% completed.</li> <li>▪ Sixth floor 50% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 85% completed.</li> <li>▪ Sixth floor 50% completed.</li> </ul> </li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 90% completed.</li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab - R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 100% completed.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Ninth floor 95% completed.</li> <li>▪ Tenth floor 60% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 85% completed.</li> <li>▪ First floor to Third floor 95% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 90% completed.</li> <li>▪ Sixth floor 50% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 90% completed.</li> <li>▪ Sixth floor 50% completed.</li> </ul> </li> </ul> </li> <li>● <b>Model Flat</b> Finishing works 90% completed.</li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
C2 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Tenth floor level slab – R.C.C 100% completed.</li> <li>▪ Tenth floor Columns Concrete 90% completed.</li> <li>▪ Terrace Floor level slab – 1<sup>st</sup> Half R.C.C 100% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 2<sup>nd</sup> half of Terrace floor level slab 10% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Seventh floor 95% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor to Fourth floor 90% completed.</li> <li>▪ Fifth floor 70% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor 90% completed.</li> <li>▪ Fifth floor 70% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Tenth floor level slab - R.C.C 100% completed.</li> <li>▪ Tenth floor Columns Concrete 100% completed.</li> <li>▪ Terrace Floor level slab – 1<sup>st</sup> Half R.C.C 100% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 2<sup>nd</sup> half of Terrace floor level slab 25% completed and balance works on progress.</li> <li>▪ Parapet Column concrete 10% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Seventh floor 95% completed.</li> <li>▪ Eighth floor 15% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor to Fourth floor 95% completed.</li> <li>▪ Fifth floor 70% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ Upto Fourth floor 95% completed.</li> <li>▪ Fifth floor 70% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> JULY -2022
C3 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Sixth Floor level slab – R.C.C 100% completed.</li> <li>▪ Sixth floor Columns Concrete 100% completed.</li> <li>▪ Seventh floor level slab – 1<sup>st</sup> Half R.C.C 100% completed.</li> <li>▪ Seventh floor Column Concrete 50% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Barbending works for 2<sup>nd</sup> half of Seventh floor level slab 80% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 90% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 50% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 90% completed.</li> <li>▪ Third floor 50% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 15% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Sixth Floor level slab – R.C.C 100% completed.</li> <li>▪ Sixth floor Columns Concrete 100% completed.</li> <li>▪ Seventh floor level slab – 1<sup>st</sup> Half R.C.C 100% completed.</li> <li>▪ Seventh floor Column Concrete 50% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Barbending works for 2<sup>nd</sup> half of Seventh floor level slab 80% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 90% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 60% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 90% completed.</li> <li>▪ Third floor 50% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 15% completed.</li> </ul> </li> </ul> </li> </ul>





**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

BLOCK	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 31 <sup>st</sup> JULY -2022
D1 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Seventh floor level slab – R.C.C 100% completed.</li> <li>▪ Seventh floor Columns Concrete 100% completed.</li> <li>▪ Eighth Floor level slab - 1<sup>st</sup> Half R.C.C 100% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Barbending works for 2<sup>nd</sup> half of Eighth floor level slab 25% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 90% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 10% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 70% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 60% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Seventh floor level slab – R.C.C 100% completed.</li> <li>▪ Seventh floor Columns Concrete 100% completed.</li> <li>▪ Eighth Floor level slab - 1<sup>st</sup> Half R.C.C 100% completed.</li> <li>▪ Eighth floor Columns concrete 45% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering &amp; Barbending works for 2<sup>nd</sup> half of Eighth floor level slab 85% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 90% completed.</li> <li>▪ Fourth floor 90% completed.</li> <li>▪ Fifth floor 70% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> <li>▪ Second floor 70% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 90% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
D2 BLOCK	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab – R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 80% completed.</li> </ul> </li> </ul> </li>   <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Fifth floor 95% completed.</li> <li>▪ Sixth floor to Ninth floor 90% completed.</li> <li>▪ Tenth floor 60% completed</li> <li>▪ Terrace floor Parapet wall 50% completed.</li> </ul> </li>   <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 80% completed.</li> <li>▪ First floor &amp; Second floor 90% completed.</li> <li>▪ Third floor &amp; Fourth floor 70% completed.</li> <li>▪ Fifth floor 50% completed.</li> <li>▪ Sixth floor 15% completed.</li> <li>▪ Seventh floor 50% completed.</li> <li>▪ Eighth floor 20% completed.</li> </ul> </li>   <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor &amp; Second floor 90% completed.</li> <li>▪ Third floor 65% completed.</li> <li>▪ Fourth floor 50% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab – R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 100% completed.</li> </ul> </li> </ul> </li>   <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Fifth floor 95% completed.</li> <li>▪ Sixth floor to Ninth floor 90% completed.</li> <li>▪ Tenth floor 60% completed</li> <li>▪ Terrace floor Parapet wall 80% completed.</li> </ul> </li>   <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 80% completed.</li> <li>▪ First floor &amp; Second floor 90% completed.</li> <li>▪ Third floor &amp; Fourth floor 70% completed.</li> <li>▪ Fifth floor 60% completed.</li> <li>▪ Sixth floor 30% completed.</li> <li>▪ Seventh floor 60% completed.</li> <li>▪ Eighth floor 60% completed.</li> <li>▪ .Ninth floor 10% completed.</li> </ul> </li>   <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor &amp; Second floor 90% completed.</li> <li>▪ Third floor 65% completed.</li> <li>▪ Fourth floor 60% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Fifth floor 50% completed.</li> <li>• <b>Model Flat</b> Finishing works 90% completed.</li> </ul>	<ul style="list-style-type: none"> <li>▪ Fifth floor 60% completed.</li> <li>▪ Sixth floor 30% completed.</li> <li>▪ Seventh floor 60% completed.</li> <li>▪ Eighth floor 60% completed.</li> <li>▪ Ninth floor 10% completed.</li> <li>• <b>Model Flat</b> Finishing works 90% completed.</li> </ul>
<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
D3 BLOCK	<ul style="list-style-type: none"> <li>• <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Ninth floor level slab – R.C.C 100% completed.</li> <li>▪ Ninth floor Columns Concrete 100% completed.</li> <li>▪ Tenth floor level slab – 1<sup>st</sup> Half R.C.C 100% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for 2<sup>nd</sup> half of Tenth floor level slab 90% completed and balance works on progress.</li> </ul> </li> </ul> </li> <li>• <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Third floor 95% completed.</li> <li>▪ Fourth floor to Seventh floor 90% completed.</li> <li>▪ Eighth floor 60% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 85% completed.</li> <li>▪ First floor to Third floor 90% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>• <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Tenth floor level slab – R.C.C 100% completed</li> <li>▪ Tenth floor Columns Concrete 35% completed.</li> </ul> </li> <li>◆ <b>On Progress</b> <ul style="list-style-type: none"> <li>▪ Shuttering works for Columns in Tenth floor level slab on progress.</li> </ul> </li> </ul> </li> <li>• <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ Upto Third floor 95% completed.</li> <li>▪ Fourth floor to Eighth floor 90% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 85% completed.</li> <li>▪ First floor to Third floor 90% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

	<ul style="list-style-type: none"> <li>▪ Fourth floor 75% completed.</li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor to Third floor 90% completed.</li> <li>▪ Fourth floor 75% completed.</li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>▪ Fourth floor 75% completed.</li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor to Third floor 90% completed.</li> <li>▪ Fourth floor 75% completed.</li> </ul> </li> </ul>
<b>BLOCK</b>	<b>STATUS UPTO PREVIOUS MONTH</b>	<b>STATUS AS ON 31<sup>st</sup> JULY -2022</b>
COMMUNITY HALL	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab – R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 90% completed.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 75% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> </ul> </li> <li>◆ <b>Ceiling Putty work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 80% completed.</li> </ul> </li> <li>◆ <b>Wall Putty work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 70% completed.</li> </ul> </li> </ul> </li> </ul>	<ul style="list-style-type: none"> <li>● <b>Structure Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Completed</b> <ul style="list-style-type: none"> <li>▪ Upto Terrace floor level slab – R.C.C 100% completed.</li> <li>▪ Terrace floor Parapet Columns Concrete 90% completed.</li> </ul> </li> </ul> </li> <li>● <b>Internal Finishing Work.</b> <ul style="list-style-type: none"> <li>◆ <b>Block Work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 90% completed.</li> </ul> </li> <li>◆ <b>Ceiling Plastering</b> <ul style="list-style-type: none"> <li>▪ Stilt floor 90% completed.</li> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> <li>▪ Third floor 10% completed.</li> </ul> </li> <li>◆ <b>Wall Plastering</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 95% completed.</li> </ul> </li> <li>◆ <b>Ceiling Putty work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 80% completed.</li> </ul> </li> <li>◆ <b>Wall Putty work</b> <ul style="list-style-type: none"> <li>▪ First floor 95% completed.</li> <li>▪ Second floor 70% completed.</li> </ul> </li> </ul> </li> </ul>



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

	<ul style="list-style-type: none"><li>◆ <b>Wall Painting work</b><ul style="list-style-type: none"><li>▪ First floor - 1st Coat painting 95% completed.</li></ul></li><li>◆ <b>Floor Tiling Work</b><ul style="list-style-type: none"><li>▪ First floor Vitrified Tile laying 95% completed.</li></ul></li><li>◆ <b>UPVC Window Fixing Work</b><ul style="list-style-type: none"><li>▪ First floor UPVC Window fixing 95% completed.</li></ul></li><li>● <b>External Finishing Work.</b><ul style="list-style-type: none"><li>◆ External Plastering<ul style="list-style-type: none"><li>▪ West Side elevation 70% completed.</li><li>▪ South Side elevation 30% completed.</li><li>▪ North Side elevation 25% completed.</li></ul></li></ul></li></ul>	<ul style="list-style-type: none"><li>◆ <b>Wall Painting work</b><ul style="list-style-type: none"><li>▪ First floor - 1st Coat painting 95% completed.</li></ul></li><li>◆ <b>Floor Tiling Work</b><ul style="list-style-type: none"><li>▪ First floor Vitrified Tile laying 95% completed.</li></ul></li><li>◆ <b>UPVC Window Fixing Work</b><ul style="list-style-type: none"><li>▪ First floor UPVC Window fixing 95% completed.</li></ul></li><li>● <b>External Finishing Work.</b><ul style="list-style-type: none"><li>◆ External Plastering<ul style="list-style-type: none"><li>▪ West Side elevation 95% completed.</li><li>▪ South Side elevation 65% completed.</li><li>▪ North Side elevation 45% completed.</li></ul></li></ul></li></ul>
--	---	---





# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

---

## PHOTOGRAPHS OF WORK PROGRESS AS ON JULY 2022

**Block A1:** Fifth Floor Level slab Concrete casting 100% completed. Shuttering works for 1<sup>st</sup> half of Sixth floor level slab 15% completed and balance works on progress.



**Block A2:** Shuttering & Barbending works for 1<sup>st</sup> half of Fifth floor level slab 70% completed.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block B1** : Parapet Column casting 100% completed. External plastering work –South Side elevation 100% completed, East side elevation 10% completed.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block B2:** Third Floor Level slab concrete casting 100% completed. Shuttering works for 1<sup>st</sup> half of Fourth floor level slab 15% completed.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block C1: Terrace Floor** level slab concrete 100% completed. Parapet Column concrete 100% completed.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block C2: Terrace floor level slab 1<sup>st</sup> half concrete casting 100% completed. Shuttering works for 2<sup>nd</sup> half 25% completed and balance works on progress.**





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block C3:** Shuttering & Barbending works for 2<sup>nd</sup> half of Seventh floor level slab 80% completed and balance works on progress.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block D1:** Shuttering & Barbending works for 2<sup>nd</sup> half of Eighth Floor level slab 85% completed and balance works on progress.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block D2: Terrace floor slab Concrete casting 100% completed. Parapet Columns concrete 100% completed. Parapet Wall Block work 80% completed.**





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Block D3:** Tenth Floor level slab Concrete casting 100% completed. Columns concrete 35% completed.



# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Community Hall:** Terrace Floor level Concrete casting 100% completed. Parapet Column concrete casting 90% completed. External Plastering in West side elevation 95% completed, South side elevation 65% completed & North side elevation 45% completed.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**View of A1 Block & A2 Block**



**View of C2 & C3 Block**





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**View of A Blocks & C Blocks**



**View of D1 Block & D2 Block**



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

**QUALITY CONTROL**

**DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:**

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			



**PROGRESS REPORT**  
**CGEWHO - CHENNAI PHASE-III PROJECT**

---

**PHOTOGRAPH OF QUALITY CONTROL AT SITE**

**Concrete Cube Compressive Strength Testing**





# **PROGRESS REPORT** **CGEWHO - CHENNAI PHASE-III PROJECT**

---

## **20mm & 12mm Aggregate Sieve Analysis Testing**



# **PROGRESS REPORT** **CGEWHO - CHENNAI PHASE-III PROJECT**

---

## **Fine Aggregate Sieve Analysis Testing**



**PROGRESS REPORT**  
**CGEWHO – CHENNAI PHASE-III PROJECT**

---

**CGEWHO – CHENNAI PHASE-III  
PROJECT**



**3<sup>rd</sup> Project Monitoring Committee  
(P.M.C) meeting Photographs**

**Meeting date : 29.07.2022**





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**Arrival of Sh. Dinesh Kapila, CEO CGEWHO at Chennai Phase-III Project Office**



**CEO,CGEWHO honoured by Sh. Vikram Rao, Technical Director M/s Srico Project pvt ltd  
Member present Centre – Sh. Mahesh, Project Manager, Chennai Phase-III project.  
Right –Sh.Vishweshwar, Principal Architect Designers workshop.**



# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Sh. Gagan Gupta, Director Technical, CGEWHO arrived Chennai Phase-III Project along with CEO, CGEWHO.



Director Technical & CEO,CGEWHO assembled for P.M.C meeting in Conference Hall.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

P.M.C elected members assembled for Meeting in Conference hall. Members present From Left - Sh. Sangameshwaran, Sh. Vishnuvardhan, Smt. V.Chandra Mahadevan & Sh. Ravi. Front row, from left – Project Manager, CGEWHO, Technical Director M/s Srco Projects & Sh.Srinivasa Rao, Managing Director M/s Srco Projects




Other members assembled at Conference hall. Members present From Right-Smt. Renu Khanna, Proprietor & Sh.Nakul Khanna, Consultant of M/s Renukhanna & associates ( Project Management Consultancy ) , Architect Designerz workshop (M/s Srco Projects)



# PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Presentation done by Architect in Meeting – Site Plan Details briefed to CEO,CGEWHO

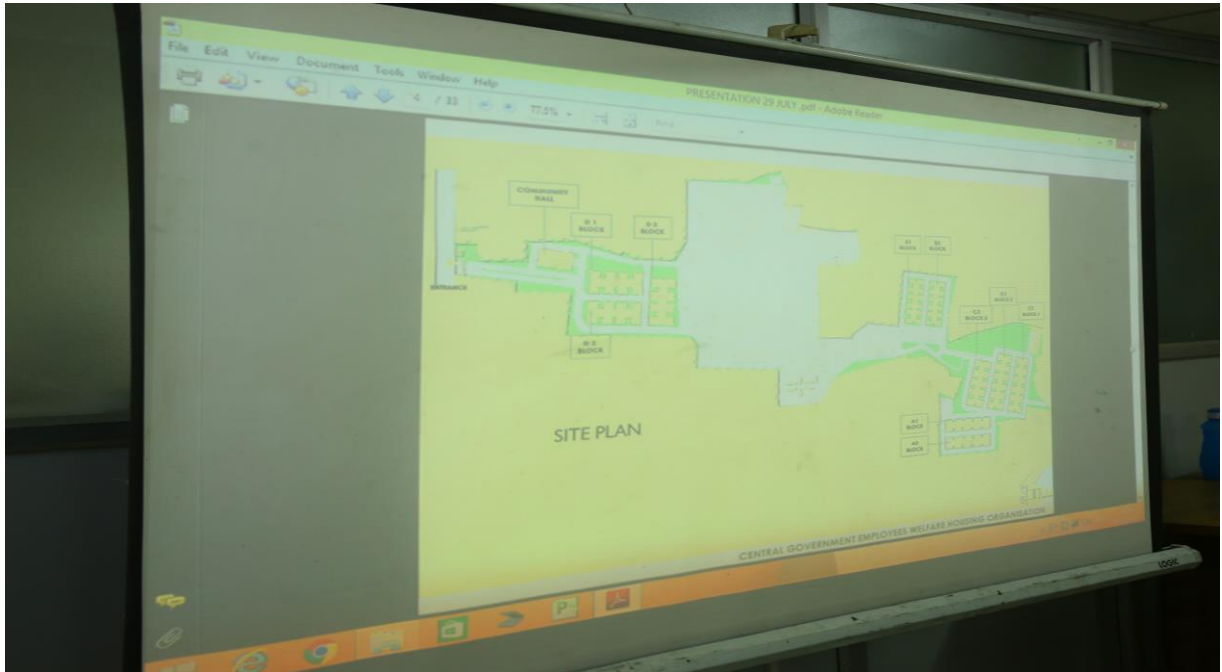

Revised Schedule for completion of work for all blocks displayed.

S.NO	BLOCK	COMPLETION TIME (MONTHS)	START DATE	LAST DATE	TOTAL	PROGRESS AS PER YARDSTICK		PROGRESS AS PER SITE CONDITION		REMARKS or % work completion
						COMPLETED	BALANCE WORK	COMPLETED	BALANCE WORK	
1	A1 block	11	01/08/22	30/06/23	100.00%	28.45%	71.55%	35.20%	64.80%	90% by June 2023
2	A2 block	12	10/07/22	30/06/23	100.00%	25.84%	74.16%	33.51%	66.49%	90% by June 2023
3	B1 block	8	11/08/22	19/04/23	100.00%	59.32%	40.68%	71.14%	28.86%	100% of work will be completed
4	B2 block				100.00%	20.11%	79.89%	26.39%	73.61%	Waiting for clearance from CGEWHO
5	C1 block	10	01/08/22	20/05/23	100.00%	55.47%	44.53%	64.19%	35.81%	100% of work will be completed
6	C2 block	11	01/08/22	30/06/23	100.00%	49.60%	50.40%	58.48%	41.52%	100% of work will be completed
7	C3 block	11	01/08/22	30/06/23	100.00%	33.22%	66.78%	38.48%	61.52%	90% by June 2023
8	D1 block	11	23/07/22	30/06/23	100.00%	36.17%	63.83%	48.83%	51.17%	90% by June 2023
9	D2 block	11	17/08/22	19/05/23	100.00%	58.01%	41.99%	68.97%	31.03%	100% of work will be completed
10	D3 block	9	17/08/22	19/05/23	100.00%	49.01%	50.99%	59.88%	40.12%	100% of work will be completed
11	D5 block	11	20/07/22	03/06/23	100.00%	65.32%	34.68%	68.84%	31.16%	100% of work will be completed
	Community Hall	8	20/07/22	15/03/23	100.00%					





# **PROGRESS REPORT** **CGEWHO - CHENNAI PHASE-III PROJECT**

Project Completion schedule has been analysed based on present status of all Blocks





# **PROGRESS REPORT** **CGEWHO - CHENNAI PHASE-III PROJECT**

---

**Few Beneficiaries of Chennai Phase-III Project came for P.M.C Meeting**





## **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

Beneficiaries nearly 15 members have been assembled for final briefing of the discussions made in the Meeting by Director Technical, CGEWHO.





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

**After Meeting – Discussions and Site visit by all members.**





# **PROGRESS REPORT** **CGEWHO – CHENNAI PHASE-III PROJECT**

---

