

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 30.06.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

30.06.2024

BLOCK	STATUS AS ON 30 th JUNE-2024
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Works <ul style="list-style-type: none"> a) Over Head Water Tanks (2 / 2) ▪ Fixing of Bathroom Wall Tiles 100% completed (200/200) ▪ Fixing of Toilet Wall Tiles 100% completed (200/200) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 100% completed (200/200) b) Ceramic Tiles in Toilets 100% completed (200/200) ▪ Vitrified Tiles in Halls & Bedrooms 100% completed (200/200). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 100% completed (2 / 2). b) Terrace Water Proofing Work 100% completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (200/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) ▪ Electrical wire pulling work 100% completed (200/200). ▪ Fixing of Modular Switches & Sockets 100% completed. (200/200)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th JUNE-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Door Shutters 99% completed (1192/1200). ▪ Fixing of UPVC Windows 96% completed (773 /800) <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. <ul style="list-style-type: none"> a) Lift 1 – Work started. ▪ Fire fighting works 17% completed. <p>➤ Model Flat Finishing works 90% completed.</p>	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Door Shutters 100% completed (1200/1200). ▪ Fixing of UPVC Windows 99% completed (794 /800) <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. <ul style="list-style-type: none"> a) Lift 1 – Work started. ▪ Fire fighting works 31% completed. <p>➤ Model Flat Finishing works 90% completed.</p>
BLOCK	STATUS AS ON 30 th JUNE-2024	
A2 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> ● Base Slab Concrete 2 out of 2 ● Tank Wall Concrete 2 out of 2 ● Top Cover slab Concrete 2 out of 2 <ul style="list-style-type: none"> ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 100% completed (2 / 2) b) Terrace Water proofing 100% completed. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th JUNE-2024
<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Bathroom Wall Tiles 99% completed (198/200). ▪ Fixing of Toilet Wall Tiles 99% completed (198/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 99% completed (198/200) b) Ceramic Tiles in Toilet 99% completed (198/200). ▪ Vitrified Tiles in Halls & Bedrooms 99% completed. (198/200). ▪ Fixing of Door Shutters 95% completed (1150/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 98% completed (195/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 17% completed. ▪ Electrical wire pulling work started (10/200). ▪ Fixing of Modular Switches & Sockets started. (10/200) 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Bathroom Wall Tiles 99% completed (198/200). ▪ Fixing of Toilet Wall Tiles 99% completed (198/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 99% completed (198/200) b) Ceramic Tiles in Toilet 99% completed (198/200). ▪ Vitrified Tiles in Halls & Bedrooms 99% completed. (198/200). ▪ Fixing of Door Shutters 100% completed (1200/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (200/200). b) Laying of Granite Countertop 100% completed (200/200). c) Fixing of S.S Sink 100% completed (200/200) <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 31% completed. ▪ Electrical wire pulling work 100% completed (200/200). ▪ Fixing of Modular Switches & Sockets 50% completed (100/200)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th JUNE-2024
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. ▪ Fixing of Door Shutters 100% completed (840/840). ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
BI BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 95% completed. ▪ Firefighting works 91% completed. ▪ Terrace Water supply Ring main works 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers on progress. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 100% completed. ▪ Firefighting works 95% completed. ▪ Terrace Water supply Ring main works 95% completed. ▪ Construction of Earth Pit chambers 90% completed ◆ Works On Progress <ul style="list-style-type: none"> ▪ Electrical Panel room- Trench works & cable tray fixing works 75% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Terrace floor level slab R.C.C ▪ Parapet Columns Concrete 100% completed ▪ Block work upto Tenth floor. ▪ Ceiling plastering upto Ninth floor. ▪ Wall plastering upto Ninth floor. ▪ 1st Coat Wall Putty upto Fifth floor completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Ninth floor 100% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Ninth floor 100% completed ▪ Electrical conducting works 93% completed. (112/120) 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Tenth floor 90% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Tenth floor 80% completed ▪ Electrical conducting works 93% completed. (112/120)



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ 1st Coat Wall Putty in Sixth floor 45% completed. ▪ Fixing of Internal Water supply pipeline (CPVC) 83% completed (100 / 120) ▪ Fixing of Internal Sanitary lines (PVC) 16% completed.(20 / 120) ▪ External Plastering 20% completed. 	<ul style="list-style-type: none"> ▪ 1st Coat Wall Putty upto Eighth floor 45% completed. ▪ Fixing of Internal Water supply pipeline (CPVC) 93% completed (112 / 120) ▪ Fixing of Internal Sanitary lines (PVC) 16% completed.(20 / 120) ▪ External Plastering 35% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Fixing of Door Shutters 100% completed (1080 / 1080) ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) ▪ Terrace Water supply Ring main works 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
C1 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting works 85% completed. ▪ Laying of External Sewerage lines 80% completed. ▪ Laying of External water supply lines 80% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers on progress. • Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 95% completed. ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External water supply lines 90% completed. ▪ Construction of Earth Pit chambers 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting works 93% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 85% completed. • Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. 	



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<ul style="list-style-type: none"> ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) ▪ Laying of Green marble for Staircase 100% completed.. ▪ Electrical wire pulling 100% completed (120 /120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85%



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<p>completed.</p> <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fire fighting works 57% completed. ▪ Terrace Water supply Ring main works 80% completed. ▪ Laying of External Sewerage lines 75% completed. ▪ Laying of External water supply lines 50% completed. 	<p>completed.</p> <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. ▪ Lift Cladding work 100% completed. ▪ Terrace Water supply Ring main works 90% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fire fighting works 60% completed. ▪ Laying of External Sewerage lines 85% completed. ▪ Laying of External water supply lines 80% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
C3 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. 	



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) ▪ Laying of Green marble for Staircase 100% completed. ▪ Electrical wire pulling 100% completed (100 /100). ▪ Fixing of UPVC Window 100% Completed. (500 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (200 / 200). ▪ Fixing of Main Door & Internal Shutters 100% completed (900 / 900). ▪ Electrical wire pulling 100% completed (100 /100). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
	<ul style="list-style-type: none"> ◆ . 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 75% completed. 4th Lift - 45% completed. ▪ Lift Cladding work 60% completed. ▪ Fixing of Modular Switches & Sockets 85% completed. (85/100). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 75% completed. 4th Lift - 45% completed. ▪ Lift Cladding work 60% completed. ▪ Fixing of Modular Switches & Sockets 100% completed. (100/100).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fire fighting works 55% completed. ▪ Laying of External Sewerage lines 50% completed. 	<ul style="list-style-type: none"> ▪ Fire fighting works 57% completed. ▪ Laying of External Sewerage lines 70% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80) ▪ Fixing of UPVC Windows 100% completed. (400 / 400). ▪ Fixing of UPVC French Door 100% completed.(without Mosquito mesh shutter) (160 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	/ 160)	
	<ul style="list-style-type: none"> ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
D1 BLOCK	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 60% completed. ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 85% completed. b) 4th lift – 35% completed. ▪ Fire fighting works 85% completed. ▪ Laying of External Sewerage lines 95% completed ▪ Laying of External Water supply lines 95% completed. ▪ Construction of Earth Pit chambers 45% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Application of Exterior Wall Damp proof Paint 90% completed. ▪ Fire fighting works 91% completed. ▪ Laying of External Sewerage lines 95% completed ▪ Laying of External Water supply lines 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 85% completed. b) 4th lift – 40% completed. ▪ Construction of Earth Pit chambers 85% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. 	



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fire Fighting Works 100% completed. ▪ Fixing of M.S Window Safety Grills 100% completed. (320 / 320). 				
	<table border="1" style="width: 100%; border-collapse: collapse;"> <thead> <tr> <th style="width: 50%;">STATUS UPTO PREVIOUS MONTH</th> <th style="width: 50%;">STATUS AS ON 30th JUNE-2024</th> </tr> </thead> <tbody> <tr> <td style="vertical-align: top;"> <ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. </td> <td style="vertical-align: top;"> <ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. </td> </tr> </tbody> </table>	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th JUNE-2024	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed.
STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th JUNE-2024				
<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. 				



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fire Fighting Works 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 55% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works on progress. ▪ Construction of Earth Pit chambers 70% completed. • Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ▪ Fire Fighting Works 95% completed. ▪ Construction of Earth Pit chambers 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 85% completed. ▪ Electrical Panel room- Trench works & cable tray fixing works 25% completed. • Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th JUNE-2024	
D3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400) ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (160 / 160). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 85% completed (273/320). ▪ Firefighting works 85% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. ▪ Fixing of M.S Window Safety Grills 90% completed (273/320). ▪ Firefighting works 91% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th JUNE-2024	
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th JUNE-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 35% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 90% completed. ▪ Application of Exterior Wall Damp proof Paint 45% completed. 	<ul style="list-style-type: none"> ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 95% completed. <p>◆ Works On Progress</p> <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 40% completed. ▪ Application of Exterior Wall Damp proof Paint 50% completed.
--	--	--

	STATUS AS ON 30th JUNE-2024
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none"> ➤ Underground Sump-1 (Near B-Block) <ul style="list-style-type: none"> ▪ Base Slab R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering – 100% completed. ▪ Pump room Inner plastering – 100% completed. ➤ Underground Sump-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base Slab - R.C.C 100% completed. ▪ Sump Wall - R.C.C 100% completed. ▪ Top slab R.C.C 100% completed. ▪ Outer Wall Waterproof plastering – 100% completed. ▪ Inner Wall Waterproof plastering 100% completed. ▪ Pump room Inner plastering 100% completed. ➤ Sewage Treatment Plant-2 (Near D-Block) <ul style="list-style-type: none"> ▪ Base slab – R.C.C 100% completed. ▪ STP Wall – R.C.C 100% completed. ▪ STP Top Slab – R.C.C 100% completed. ▪ STP Pump Room completed. ▪ Outer wall Waterproof plastering 100% completed. ▪ Inner Wall Waterproof plastering 100% completed. ▪ Installation of STP 85% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none">➤ Sewage Treatment Plant-1 (Near C3-Block)<ul style="list-style-type: none">▪ Excavation Work completed.▪ Base slab RCC completed.▪ STP Wall Reinforcement 100% completed.▪ STP Wall Concrete 65% completed.➤ Laying of External Sewer lines<ul style="list-style-type: none">▪ Type D All Blocks – 95% completed.▪ C1 Block – 90% completed▪ C2 Block – 85% completed.▪ C3 Block – 70% completed.➤ Laying of External Water Supply lines<ul style="list-style-type: none">▪ Type D All Blocks – 95% completed.▪ C1 Block – 90% completed▪ C2 Block – 80% completed.➤ Laying of Storm Water Drainage.<ul style="list-style-type: none">▪ Type D All Blocks – 85% completed.
--	--

PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPHS OF WORK PROGRESS AS ON 30th JUNE 2024

Community Hall: Lift Commissioning works on progress. Lift -1 - Test Run done.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: False ceiling works on progress. Firefighting Ring main works completed at Terrace



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block A2 : UPVC Windows fixing on progress, Lift Erection works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Fixing of Electrical Panel on progress. Connection of Sewage lines to chamber at Stilts on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B2 : Core cutting & fixing of PVC pipes for internal sanitary lines and Water proofing works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block C1: Electrical wire pulling in Corridor & fixing of Architrave putty for Door frames on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Fixing of Electrical Panels & Firefighting cabling works for Fire alarm on progress.

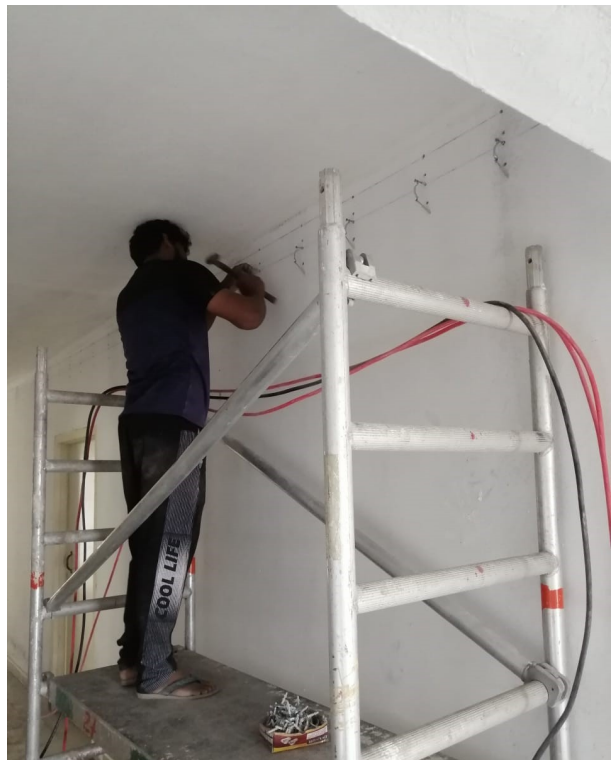

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Lift cladding works & External painting works on progress



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: Fixing of Electrical Panel in Stilts on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D2: Fixing of Electrical panels on progress. Laying of Grano flooring at stilts on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Fixing of Electrical Panels at stilts on progress. External Painting work on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

U.G Sump 1 (Near B Block) – All RCC works completed. Internal Waterproofing work in Sump & Pump room completed.



U.G Sump 2 (Near D Block) – All RCC works completed. Water proofing works completed. Fixing of Ladder on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Sewage Treatment Plant 2 (Near D Block). All RCC works completed. Internal Water proof plastering works 100% completed. Installation of STP 85% completed.



Sewage Treatment Plant 1 (Near C Block). Base slab RCC completed. Wall Concrete 60% completed. Shuttering work for balance wall portion on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

External Sewerage Lines : Laying of External Sewage line & construction of Chambers around C3 & B1 block on progress.



C3 – BLOCK



B1 - BLOCK

Storm Water Drainage: Masonry work for Strom water Drainage around D1 & C2 blocks on progress.



D1- BLOCK



C2- BLOCK

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

