

**CGEWHO – CHENNAI PHASE-III
PROJECT**



MONTHLY PROGRESS REPORT

STATUS AS ON : 30.04.2024

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

30.04.2024

BLOCK	STATUS AS ON 30 th APRIL-2024	
A1 BLOCK	<p>◆ 100% Completed Works</p> <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor ▪ Electrical Conducting works in Tenth floor. ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th APRIL-2024
	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Bathroom Wall Tiles 94% completed (188/200). ▪ Fixing of Toilet Wall Tiles 94% completed (188/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 94% completed (188/200) b) Ceramic Tiles in Toilets 94% completed (188/200) ▪ Vitrified Tiles in Halls & Bedrooms 94% completed (188/200). 	<p>◆ 90% Completed Works</p> <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External Plastering 95% completed in all sides. ▪ Fixing of Staircase Handrail 95% completed. ▪ Fixing of Bathroom Wall Tiles 99% completed (198/200). ▪ Fixing of Toilet Wall Tiles 99% completed (198/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathrooms 99% completed (198/200) b) Ceramic Tiles in Toilets 99% completed (198/200) ▪ Vitrified Tiles in Halls & Bedrooms 99% completed (198/200).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 50% completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 94% completed (188/200). b) Laying of Granite Countertop 94% completed (188/200). c) Fixing of S.S Sink 94% completed (188/200) ▪ Fixing of Door Shutters 89% completed (1068/1200). ▪ Fixing of UPVC Windows 74% completed (590 /800) ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ▪ Fire fighting works 15% completed. ➤ Model Flat Finishing works 90% completed. 	<ul style="list-style-type: none"> ▪ Fixing of Door Shutters 94% completed (1134/1200). ▪ Fixing of UPVC Windows 95% completed (760 /800) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 95% completed (190/200). b) Laying of Granite Countertop 95% completed (190/200). c) Fixing of S.S Sink 95% completed (190/200) ◆ Works On Progress <ul style="list-style-type: none"> ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace Water Proofing 80% completed. ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 15% completed. ▪ Electrical wire pulling work 55% completed (110/200). ▪ Fixing of Modular Switches & Sockets 55% completed. (110/120) ➤ Model Flat Finishing works 90% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
A2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete 2 out of 2 (b) Tank Wall Concrete 2 out of 2 (c) Top Cover slab Concrete 2 out of 2 ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Electrical Conducting works upto Tenth floor. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Water supply pipe Lines (CPVC). ▪ Fixing of Sanitary Lines (PVC). ▪ Fixing of Vertical Plumbing Lines in Shaft. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles 73% completed (146/200). ▪ Fixing of Toilet Wall Tiles 73% completed (146/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 73% completed (146/200) b) Ceramic Tiles in Toilet 73% completed (146/200) ▪ Vitrified Tiles in Halls & Bedrooms 70% completed. (140/200). ▪ Fixing of Door Shutters 59% completed (708/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 24% completed (47/200). b) Laying of Granite Countertop 24% completed (47/200). c) Fixing of S.S Sink 24% completed (47/200) ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 50% completed (1 / 2) b) Terrace Water proofing 30% completed. ▪ Lift Materials 4 out of 4 received. Shaft work on progress. ▪ Fire fighting works 15% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Fixing of Bathroom Wall Tiles 94% completed (188/200). ▪ Fixing of Toilet Wall Tiles 94% completed (188/200). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 94% completed (188/200) b) Ceramic Tiles in Toilet 94% completed (188/200). ▪ Vitrified Tiles in Halls & Bedrooms 93% completed. (186/200). ▪ Water Proofing Work <ul style="list-style-type: none"> a) Over Head Water Tank 100% completed (2 / 2) b) Terrace Water proofing 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Door Shutters 89% completed (1069/1200). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 53% completed (106/200). b) Laying of Granite Countertop 67% completed (135/200). c) Fixing of S.S Sink 67% completed (135/200) ▪ Lift Materials 4 out of 4 received. Bulket fittings completed. ▪ Fire fighting works 15% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th APRIL-2024
B1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. ▪ Fixing of Door Shutters 100% completed (840/840). ▪ Electrical wire pulling work 100% completed (120/120).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BI BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 93% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Firefighting works 75% completed. ▪ Terrace Water supply Ring main works 50% completed. ▪ Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 3 out 3. ▪ Lift Cladding works 3 out of 3. ▪ Laying of Green marble for Staircase 100% completed. ▪ Application of Exterior Wall Primer ▪ Fixing of M.S Window Safety Grills 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Firefighting works 88% completed. ▪ Terrace Water supply Ring main works 80% completed. • Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
B2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Upto Terrace floor level slab R.C.C ▪ Parapet Columns Concrete 100% completed ▪ Block work upto Ninth floor. ▪ Ceiling plastering upto Eighth floor. ▪ Wall plastering upto Eighth floor. ▪ 1st Coat Wall Putty upto Fifth floor completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Shuttering & Reinforcement works for 2nd Half of Terrace Floor level slab 98% completed. ▪ Block work <ul style="list-style-type: none"> a) In Ninth floor 90% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Ninth floor 70% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Ninth floor 70% completed ▪ Electrical conducting works 70% completed. 	<ul style="list-style-type: none"> ◆ Works On Progress <ul style="list-style-type: none"> ▪ Terrace floor level slab RCC 100% completed. ▪ Block work <ul style="list-style-type: none"> a) In Tenth floor 60% completed. ▪ Ceiling Plastering <ul style="list-style-type: none"> a) In Ninth floor 85% completed. ▪ Wall Plastering <ul style="list-style-type: none"> a) In Ninth floor 85% completed ▪ Electrical conducting works 80% completed. ▪ 1st Coat Wall Putty in Sixth floor 15% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

		<ul style="list-style-type: none"> ▪ Fixing of Internal Water supply pipeline (CPVC) 80% completed (96 / 120) ▪ External Plastering 15% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
C1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Internal Plumbing Line. <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of UPVC Windows. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank b) Terrace floor Water proofing. ▪ Laying of Green marble for Staircase. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. b) Laying of Granite Countertop. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C1 BLOCK	<ul style="list-style-type: none"> c) Fixing of S.S Sink. ▪ Lift Cladding works 4 out of 4. ▪ Fixing of Door Shutters 100% completed (1080 / 1080) ▪ Electrical wire pulling work 100% completed (120/120). ▪ Fixing of Modular Switches & Sockets 100% completed. (120/120) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails 3 out of 3 ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Terrace Water supply Ring main works 90% completed ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of M.S Window Safety Grills 85% completed. ▪ Fire Fighting works 52% completed. ● Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Staircase Hand Rails (3 out of 3) 95% completed. ▪ Lift Installation works 4 out 4. ▪ Application of Exterior Wall Primer. ▪ Terrace Water supply Ring main works 95% completed. ▪ Fixing of M.S Window Safety Grills 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire Fighting works 78% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
C2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) (b) Wall Concrete (2 out of 3) (c) Top Cover slab (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C2 BLOCK	<ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 ▪ Fixing of Bathroom Wall Tiles completed. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom completed. b) Vitrified Tiles in Halls & Bedrooms completed. c) Vitrified Tiles in Corridor completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (120 / 120) b) Laying of Granite Countertop 100% completed. (120 / 120). c) Fixing of S.S Sink 100% completed. (120 / 120). ▪ Fixing of UPVC Window 100% completed. (600 / 600) ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed. (240 /240) ▪ Fixing of Main Door & Internal Shutters 100% completed (1080 / 1080) ▪ Laying of Green marble for Staircase 100% completed.. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 90% completed. ▪ Electrical wire pulling 90% completed (109 /120). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 45% completed. ▪ Fixing of Modular Switches & Sockets 55% completed. (66/120). ▪ Terrace Water supply Ring main works 55% completed 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Application of Exterior Wall Primer ▪ Lift Installation works 4 out 4 - 85% completed. ▪ Water Proofing Works. <ul style="list-style-type: none"> a)Terrace floor Water proofing 95% completed. ▪ Lift Cladding work 90% completed. ▪ Electrical wire pulling 100% completed (120 /120). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fire fighting works 54% completed. ▪ Fixing of Modular Switches & Sockets 84% completed. (101/120). ▪ Terrace Water supply Ring main works 75% completed



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30 th APRIL-2024	
C3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (2 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank (2 / 2) completed. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed (100/100) b) Laying of Granite Countertop 100% completed. (100/100). c) Fixing of S.S Sink 100% completed. (100/ 100). ▪ Fixing of Bathroom Wall Tiles 100% completed. (300 /300) ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (300 /300) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (100 / 100) ▪ Laying of Green marble for Staircase 100% completed. ▪ Electrical wire pulling 100% completed (100 /100). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30 th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ 2nd Coat Wall Putty 90% completed. (90 /100). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails. ▪ Application of Exterior Wall Primer ▪ 2nd Coat Wall Putty 100% completed. (100 /100).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

C3 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of UPVC Window 97% Completed. (487 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 98% completed (197 / 200). ▪ Fixing of Main Door & Internal Shutters 99% completed (898 / 900). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 30% completed. 4th Lift - 15% completed. ▪ Lift Cladding work 50% completed. ▪ Electrical wire pulling 50% completed (50 /100). ▪ Fixing of Modular Switches & Sockets 43% completed. (43/100). ▪ Fire fighting works 45% completed. 	<ul style="list-style-type: none"> ▪ Fixing of UPVC Window 100% Completed. (500 / 500). ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (200 / 200). ▪ Fixing of Main Door & Internal Shutters 100% completed (900 / 900) ▪ Water Proofing Works. <ul style="list-style-type: none"> a)Terrace floor Water proofing 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works – <ul style="list-style-type: none"> 2 Lifts - 85% completed. 3rd Lift - 45% completed. 4th Lift - 30% completed. ▪ Lift Cladding work 50% completed. ▪ Electrical wire pulling 100% completed (100 /100). ▪ Fixing of Modular Switches & Sockets 70% completed. (70/100). ▪ Fire fighting works 54% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
D1 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty 100% completed. (80 /80). ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 3 out of 3 b) Terrace floor Water proofing 100% completed. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D1 BLOCK	<ul style="list-style-type: none"> ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80). ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). c) Fixing of S.S Sink 100% completed. (80 / 80). ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80) 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of UPVC Windows 99% completed. (398 / 400). ▪ 2nd Coat Wall Putty 100% completed. (80 / 80). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door 99% completed.(without Mosquito mesh shutter) (159 / 160) ▪ Application of Exterior Wall Damp proof Paint 40% completed. ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 80% completed. b) 4th lift – 10% completed. ▪ Electrical Wire pulling works 50% completed. (40/ 80). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of Balcony Handrail. ▪ External plastering in all sides 95% completed. ▪ Application of External Wall Primer-1st Coat ▪ Fixing of UPVC Windows 100% completed. (400 / 400). ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door 100% completed.(without Mosquito mesh shutter) (160 / 160) ▪ Application of Exterior Wall Damp proof Paint 50% completed. ▪ Lift Installation works <ul style="list-style-type: none"> a) 3 out 4 - 85% completed. b) 4th lift – 25% completed. ▪ Electrical Wire pulling works 100% completed. (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Modular Switches & Sockets 50% completed. (40/80). ▪ Fire fighting works 75% completed. ▪ Laying of External Sewerage lines 85% completed ▪ Laying of External Water supply lines 90% completed. 	<ul style="list-style-type: none"> ▪ Fire fighting works 77% completed. ▪ Laying of External Sewerage lines 90% completed ▪ Laying of External Water supply lines 90% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
D2 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (3 out of 3) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom b) Vitrified Tiles in Halls & Bedrooms. c) Vitrified Tiles in Corridor. ▪ Fixing of UPVC Windows. ▪ Fixing of Main Door & Internal Shutters. ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados. 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D2 BLOCK	<ul style="list-style-type: none"> b) Laying of Granite Countertop. c) Fixing of S.S Sink. ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank ▪ Laying of Green marble for Staircase. ▪ Fixing of UPVC French Door (without Mosquito mesh shutter). ▪ Electrical Wire pulling works 100% completed (80/ 80). ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Fire Fighting Works 100% completed. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 90% completed. (290 / 320). ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External Water supply lines 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Laying of Storm Water drain pipes 90% completed. ▪ Application of Exterior Wall Damp proof Paint 15% completed. ▪ Fire Fighting Works 95% completed. ▪ Model Flat Finishing works 95% completed. 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fixing of M.S Window Safety Grills 98% completed. (315 / 320). ▪ Laying of External Sewerage lines 95% completed. ▪ Laying of External Water supply lines 95% completed. ▪ Laying of Storm Water drain pipes 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Application of Exterior Wall Damp proof Paint 45% completed. ▪ Fire Fighting Works 95% completed. ● Model Flat Finishing works 95% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
D3 BLOCK	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (4 out of 4) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (3 out of 3) 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> (b) Wall Concrete (3 out of 3) (c) Top Cover slab (3 out of 3) ▪ Block work upto Tenth floor & Parapet wall. ▪ Ceiling Plastering upto Tenth floor. ▪ Wall plastering upto Tenth floor. ▪ 1st Coat Wall Putty upto Tenth floor. ▪ 2nd Coat Wall Putty upto Tenth floor ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Over Head Water Tank 1 out of 3 ▪ Fixing of Bathroom Wall Tiles 100% completed. (320 / 320) ▪ Kitchen Finishing Works <ul style="list-style-type: none"> a) Fixing of Wall Dados 100% completed. (80 / 80) b) Laying of Granite Countertop 100% completed. (80 / 80). ▪ Fixing of S.S Sink 100% completed. (80 / 80). ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Ceramic Tiles in Bathroom 100% completed. (320 / 320) b) Vitrified Tiles in Halls & Bedrooms 100% completed. (80 / 80) c) Vitrified Tiles in Corridor 100% completed. ▪ Fixing of Main Door & Internal Shutters 100% completed (880 / 880) ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing 100% completed. b) Over Head Water Tank 3 out of 3 completed. ▪ Fixing of UPVC Windows 100% completed. (400 / 400) ▪ Electrical Wire pulling works 100% completed (80/ 80). 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (160 / 160). 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Fixing of UPVC French Door (without Mosquito mesh shutter) 100% completed (160 / 160).



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

D3 BLOCK	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Fixing of Modular Switches & Sockets 93% completed. (75/80). ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External water supply lines 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 62% completed (200/320). ▪ Firefighting works 75% completed. 	<ul style="list-style-type: none"> ▪ Laying of Green marble for Staircase. ▪ Lift Cladding works 90% completed. ▪ Fixing of Modular Switches & Sockets 100% completed. (80/80). ▪ Application of Exterior Wall Primer ▪ Laying of External Sewerage lines 90% completed. ▪ Laying of External water supply lines 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Lift Installation works - 4 out of 4 - 85% completed. ▪ Fixing of M.S Window Safety Grills 78% completed (250/320). ▪ Firefighting works 77% completed.
BLOCK	STATUS AS ON 30th APRIL-2024	
COMMUNITY HALL	<ul style="list-style-type: none"> ◆ 100% Completed Works <ul style="list-style-type: none"> ▪ Terrace floor level slab R.C.C ▪ Terrace floor Parapet Columns Concrete. ▪ Lift Head room (2 out of 2) - Slab Concrete. ▪ Over Head Water Tank <ul style="list-style-type: none"> (a) Base Slab Concrete (b) Tank Wall Concrete (c) Top Cover slab Concrete. ▪ Block work upto Fourth floor & Parapet wall. ▪ Ceiling Plastering upto Fourth floor. ▪ Wall plastering upto Fourth floor. ▪ 1st Coat Wall Putty upto Fourth floor. ▪ 2nd Coat Wall Putty upto Fourth floor. ▪ Fixing of Balcony Handrail. ▪ Fixing of Staircase Hand Rails ▪ Fixing of Internal Plumbing Line <ul style="list-style-type: none"> a) Water supply pipe Lines (CPVC). b) Sanitary Lines (PVC) ▪ Fixing of Vertical Plumbing Line in Shafts <ul style="list-style-type: none"> a) Water supply pipe Lines (G.I). b) Sanitary Lines (PVC). 	



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> ▪ Fixing of Bathroom Wall Tiles. ▪ Laying Of Floor Tiles <ul style="list-style-type: none"> a) Vitrified Floor Tiles in Hall & rooms b) Ceramic Floor Tiles in Bathrooms. c) Kota Stone in Staircase & Lobby ▪ Fixing of UPVC Windows. ▪ Fixing of Wooden flush Door for rooms. ▪ Fixing of Fire Safety Door for Hall Main Entrance ▪ External Plastering in all sides. ▪ Water Proofing Works. <ul style="list-style-type: none"> a) Terrace floor Water proofing. b) Over Head Water Tank. 	
	STATUS UPTO PREVIOUS MONTH	STATUS AS ON 30th APRIL-2024
	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 90% completed. ▪ Electrical Wire & cables pulling work 90% completed. ▪ Fixing of Modular Switches & Sockets 90% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures. ▪ Excavation for laying of Firefighting Hydrant pipes on progress 	<ul style="list-style-type: none"> ◆ 90% Completed Works <ul style="list-style-type: none"> ▪ Lift Installation works 4 out 4. ▪ Lift Cladding works 4 out of 4. ▪ Application of Exterior Wall Primer. ▪ Fire fighting works – Installation of Pipelines 95% completed. ▪ Electrical Wire & cables pulling work 95% completed. ▪ Fixing of Modular Switches & Sockets 95% completed. ◆ Works On Progress <ul style="list-style-type: none"> ▪ Fixing of Sanitary fixtures 20% completed. ▪ Excavation for laying of Firefighting Hydrant pipes 75% completed. ▪ Application of Exterior Wall Damp proof Paint 15% completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

STATUS AS ON 30 th APRIL-2024	
EXTERNAL DEVELOPMENT WORKS	<ul style="list-style-type: none">➤ Underground Sump-2 (Near D-Block)<ul style="list-style-type: none">▪ Base Slab - R.C.C 100% completed.▪ Sump Wall - R.C.C 100% completed.▪ Top slab R.C.C 100% completed.▪ Outer Wall Waterproof plastering – 100% completed.▪ Inner Wall Waterproof plastering 100% completed.▪ Pump room Inner plastering 100% completed. ➤ Underground Sump-1 (Near B-Block)<ul style="list-style-type: none">▪ Base Slab R.C.C 100% completed.▪ Sump Wall - R.C.C 100% completed.▪ Top slab R.C.C 100% completed.▪ Outer Wall Waterproof plastering – 100% completed.▪ Inner Wall Waterproof plastering – 90% completed.▪ Pump room Inner plastering – 100% completed. ➤ Sewage Treatment Plant-2 (Near D-Block)<ul style="list-style-type: none">▪ Base slab – R.C.C 100% completed.▪ STP Wall – R.C.C 100% completed.▪ STP Top Slab – R.C.C 100% completed.▪ STP Pump Room completed.▪ Outer wall Waterproof plastering 100% completed.▪ Inner Wall Waterproof plastering 100% completed.▪ Installation of STP 70% completed. ➤ Sewage Treatment Plant-1 (Near C3-Block)<ul style="list-style-type: none">▪ Excavation Work completed.▪ Base slab RCC completed.▪ STP Wall Reinforcement 85% completed.▪ STP Wall shuttering started.

PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

PHOTOGRAPHS OF WORK PROGRESS AS ON 30th APRIL 2024

Community Hall : Laying of Firefighting Hydrant Pipe 75% completed. External Painting final coat on progress.



PROGRESS REPORT


CGEWHO – CHENNAI PHASE-III PROJECT

Block A1: Fixing of UPVC Windows, laying of Kitchen Granite counter on progress.



PROGRESS REPORT CGEWHO – CHENNAI PHASE-III PROJECT

Block A2 : Fixing of Main doors & Internal doors on progress.

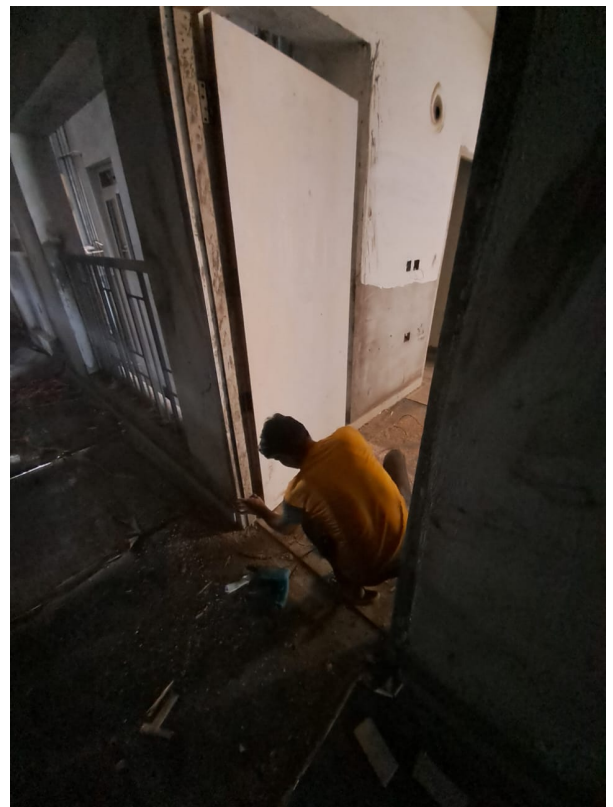

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B1: Firefighting Pump installation completed. Earth pit for Lifts on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block B2 : Terrace Floor Level slab Concrete casting 100% completed. Parapet columns 100% completed. Fixing of internal water supply lines (CPVC) on progress. External Plastering South side completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C1: Laying of External Sewerage lines & connection to shafts on progress. Excavation for laying of Storm water drainage lines on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C2: Marking & excavation for Storm water drainage works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block C3: Lift Erection Works in 3rd & 4th Lift on progress. Connection of Vertical plumbing lines to Gully chambers in Stilt floor on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D1: External Painting works on progress. Earth pit work for Lifts on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT


Block D2: Clearing & levelling in Stilt for flooring work on progress. Stilt roof Painting works on progress.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Block D3: Fixing of Electrical DB in flats & false ceiling works in Toilets on progress.

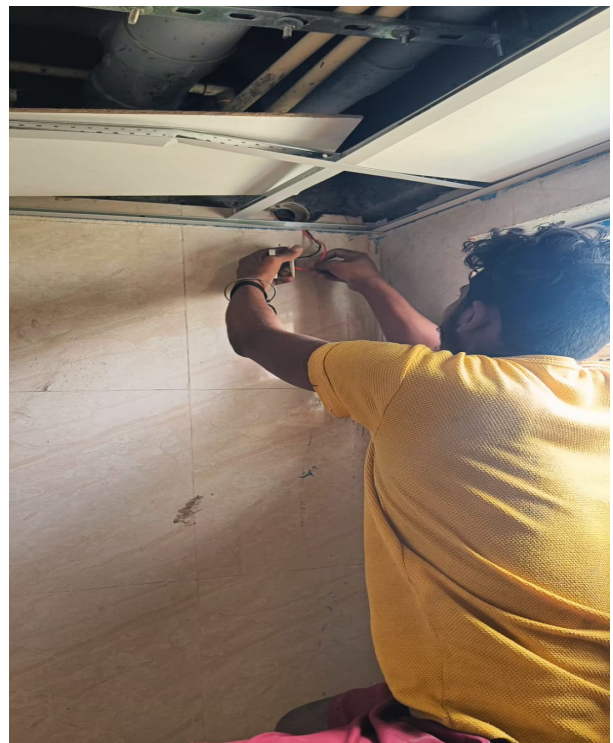

PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

U.G Sump 1 (Near B Block) – All RCC works completed. Internal Waterproofing work for Sump on progress.



U.G Sump 2 (Near D Block) – All RCC works completed. Pump room Inner plastering 100% completed & Internal Water proof plastering works 100% completed..



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

Sewage Treatment Plant 2 (Near D Block). All RCC works completed. Internal Water proof plastering works 100% completed. Installation of STP 70% completed.



Sewage Treatment Plant 1 (Near C Block). Base slab RCC completed. Reinforcement works for Wall 85% completed.



PROGRESS REPORT

CGEWHO – CHENNAI PHASE-III PROJECT

External Sewerage Lines : Laying of External Sewage line & construction of Chambers around C1 & C2 blocks on progress.



Excavation works around C3 block on progress. Connection of Sewer line to Chamber & plastering on progress.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Arcot (T.K), Ranipet (Dist) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2.	P- Sand	Uthiramerur, Kanchipuram (DT) Walajabad(T.K), Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt), Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt) Vellore Dt & Chittoor Dt.	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability of concrete.			

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

