

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

30.09.2019

BLOCK	STATUS AS ON 30.09.2019
A1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (PCC) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 100% completed • Stilt floor Columns Concrete 100% completed. • First floor level slab First Half Concrete Casting 100% Completed. • Bar Bending and Shuttering work for Second half of First Floor level slab 70% completed and balance work on progress.
BLOCK	STATUS AS ON 30.09.2019
A2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (PCC) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 80% completed • Stilt floor Columns Concrete 90% completed. • Bar Bending and Shuttering work on Progress for balance 10% Stilt floor columns. • Bar Bending and Shuttering work for First half of First Floor level slab 30% completed and balance work on progress.
BLOCK	STATUS AS ON 30.09.2019
B1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed • Columns up to Third floor Level 100%Completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor Level 100% Completed • Fourth floor level slab Concrete Casting 100% Completed. • Columns up to Fifth floor Level 100%Completed. • Fifth floor level slab Concrete Casting 100% Completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

	<ul style="list-style-type: none"> • Columns up to Sixth floor Level 100% Completed • Sixth floor level slab Concrete Casting 100% Completed. • Shuttering & Barbending work for 1st half of Seventh Floor level slab 50% completed and balance work on progress. • Block work for Model Flat at First Floor 100% completed. • Ceiling & Wall Plastering work for Model flat 100% Completed. • Finishing works for Model Flat 100% Completed.
BLOCK	STATUS AS ON 30.09.2019
B2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • PCC for pile cap 100% completed. • Pile Cap Casting 100% completed • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab First Half Concrete Casting 100% Completed. • Shuttering & Barbending work for Second Half of Second Floor Level slab 70% Completed and balance work on progress. • Shuttering & Barbending work for Columns upto Third floor on progress.
BLOCK	STATUS AS ON 30.09.2019
C1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level slab Concrete Casting 100% Completed. • Columns up to Fifth floor level 100% completed. • Fifth floor level slab Concrete Casting 100% Completed. • Columns up to Sixth floor level 100% completed. • Sixth floor level slab Concrete Casting 100% Completed. • Columns up to Seventh floor level 100% completed. • Shuttering & Barbending work for First Half of Seventh Floor Level slab 70% Completed and balance work on progress. • Block work for Model Flat at First Floor 100% completed. • Ceiling & Wall Plastering work for Model flat 100% Completed. • Finishing works for Model Flat 100% Completed.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30.09.2019
C2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second Floor level 100% Completed. • Second floor level slab Concrete Casting 100% Completed. • Columns up to Third Floor level 100% Completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth Floor level 100% Completed. • Fourth floor level slab First Half Concrete Casting 100% Completed. • Shuttering work for Second Half of Fourth floor level slab 70% completed and balance work on progress.
BLOCK	STATUS AS ON 30.09.2019
C3 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to Stilt floor level 100% completed. • PCC flooring for Stilt Floor 100% Completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab First Half Concrete Casting 100% Completed. • Shuttering & Barbending work for Second Half of Second floor level slab 50% completed and balance work on progress. • Columns up to Third floor level 30% completed. • Shuttering & Barbending work for First Half of Third floor level slab 25% completed and balance work on progress.
BLOCK	STATUS AS ON 30.09.2019
D1 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% completed. • Plain Cement Concrete (PCC) For Pile Cap work 100% completed. • Pile Chipping Work 100% completed. • Pile Cap casting 100% completed. • Earthwork backfilling 90% completed. • Plinth Beam Block work 60% completed and balance work on progress. • Stilt Floor Columns Concrete work 30% Completed & balance work on progress • Shuttering work for First half of First floor level slab 15% completed and balance work on progress. • Barbending Fabrication work for First half of First Floor level slab 10% completed and balance work on progress.



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

BLOCK	STATUS AS ON 30.09.2019
D2 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casting 100% Completed • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casting 100% Completed • Columns up to Third floor level 100% completed. • Third floor level slab Concrete Casting 100% Completed. • Columns up to Fourth floor level 100% completed. • Fourth floor level slab Concrete Casting 100% Completed. • Columns upto Fifth Floor level Slab 100% Completed. • Fifth floor level slab Concrete Casting 100% Completed. • Columns upto Sixth Floor level Slab 50% Completed. • Shuttering & Bar bending work for First half of Sixth floor level slab 60% completed and balance work on progress. • Block work for Model Flat at First Floor 100% completed. • Ceiling & Wall Plastering work for Model flat 100% Completed. • Model Flat Finishing works on progress in full swing
BLOCK	STATUS AS ON 30.09.2019
D3 BLOCK	<ul style="list-style-type: none"> • Piling work 100% completed. • Pile cap casting 100% completed. • Columns up to First floor level 100% completed. • First floor level slab Concrete Casing 100% Completed. • Columns up to Second floor level 100% completed. • Second floor level slab Concrete Casing 100% Completed. • Columns up to Third floor level 100% completed. • Third floor level Slab Concrete Casing 100% Completed. • Columns up to Fourth floor level 50% completed. • Barbending Fabrication Work on progress for balance 50% Columns upto Fourth Floor Level. • Shuttering & Barbending work for First Half of Fourth floor level slab 70% completed and balance work on progress.
BLOCK	STATUS AS ON 30.09.2019
COMMUNITY HALL	<ul style="list-style-type: none"> • Piling work 100% completed. • Earth work excavation for Pile Cap works 100% Completed. • PCC for pile cap 100% completed • Pile cap casting 100% completed. • Earthwork backfilling 100% completed • Stilt Floor Columns Concrete 100% completed. • Shuttering & Barbending work for Stilt floor roof slab 85% completed.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

PHOTOGRAPHS OF WORK PROGRESS AS ON 30.09.2019

Block A1: First Floor slab 1st Half concrete completed & Second half on progress.



Block A2 : First Floor Slab shuttering & barbending works are on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block B1: Sixth Floor slab completed & in Seventh Floor slab Suttering & Barbending works are on progress



Block B2: Second Floor slab 1st Half concrete completed & in 2nd half portion slab shuttering & barbending works are on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block C1: Sixth Floor slab completed & in Seventh Floor slab Suttering & Barbending works are on progress



Block C2: Fourth Floor slab 1st Half concrete completed & in 2nd half portion slab shuttering & barbending works are on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block C3: Second Floor 1st Half concrete completed & in 2nd half portion shuttering works are on progress. In Third Floor 1st Half Slab Shuttering & Barbending works on progress



Block D1: Pile Cap Works Complete. Earthwork backfilling & PCC for on Progress. First Floor 1st Half Slab Shuttering works are on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Block D2 : Sixth Floor slab 1st Half Portion Shuttering & Barbending works are on progress.



Block D3: Fourth Floor slab 1st Half Portion Shuttering & Barbending works are on progress.



PROGRESS REPORT **CGEWHO – CHENNAI PHASE-III PROJECT**

Community Hall : Shuttering & Barbending work for Stilt floor roof slab 85% Completed



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

QUALITY CONTROL

DURING CONSTRUCTION FOLLOWING QUALITY CONTROL TESTS CONDUCTED AT SITE:

Sl.No.	Materials	Source from	Test Done	Result
1	M-Sand	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis & Silt content
2	Coarse Aggregate (20mm)	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
3	Coarse Aggregate (12mm)	Sriperambathur, Kanchipuram (Dt)	Each Truck	Sieve Analysis
4	Cement	Third party testing is being done.		
5	Steel	Third party testing is being done.		
6	Pile Integrity	Third party testing is being done.		
7	Soil Compaction	Third party testing is being done.		
8	RCC cubes are being tested and Register is being maintained.			
9	Slump test conducted at site to insure workability if concrete.			



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT


PHOTOGRAPH OF QUALITY CONTROL AT SITE

Concrete Cube Compressive Strength Testing



PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

20mm & 12mm Aggregate Sieve Analysis Testing

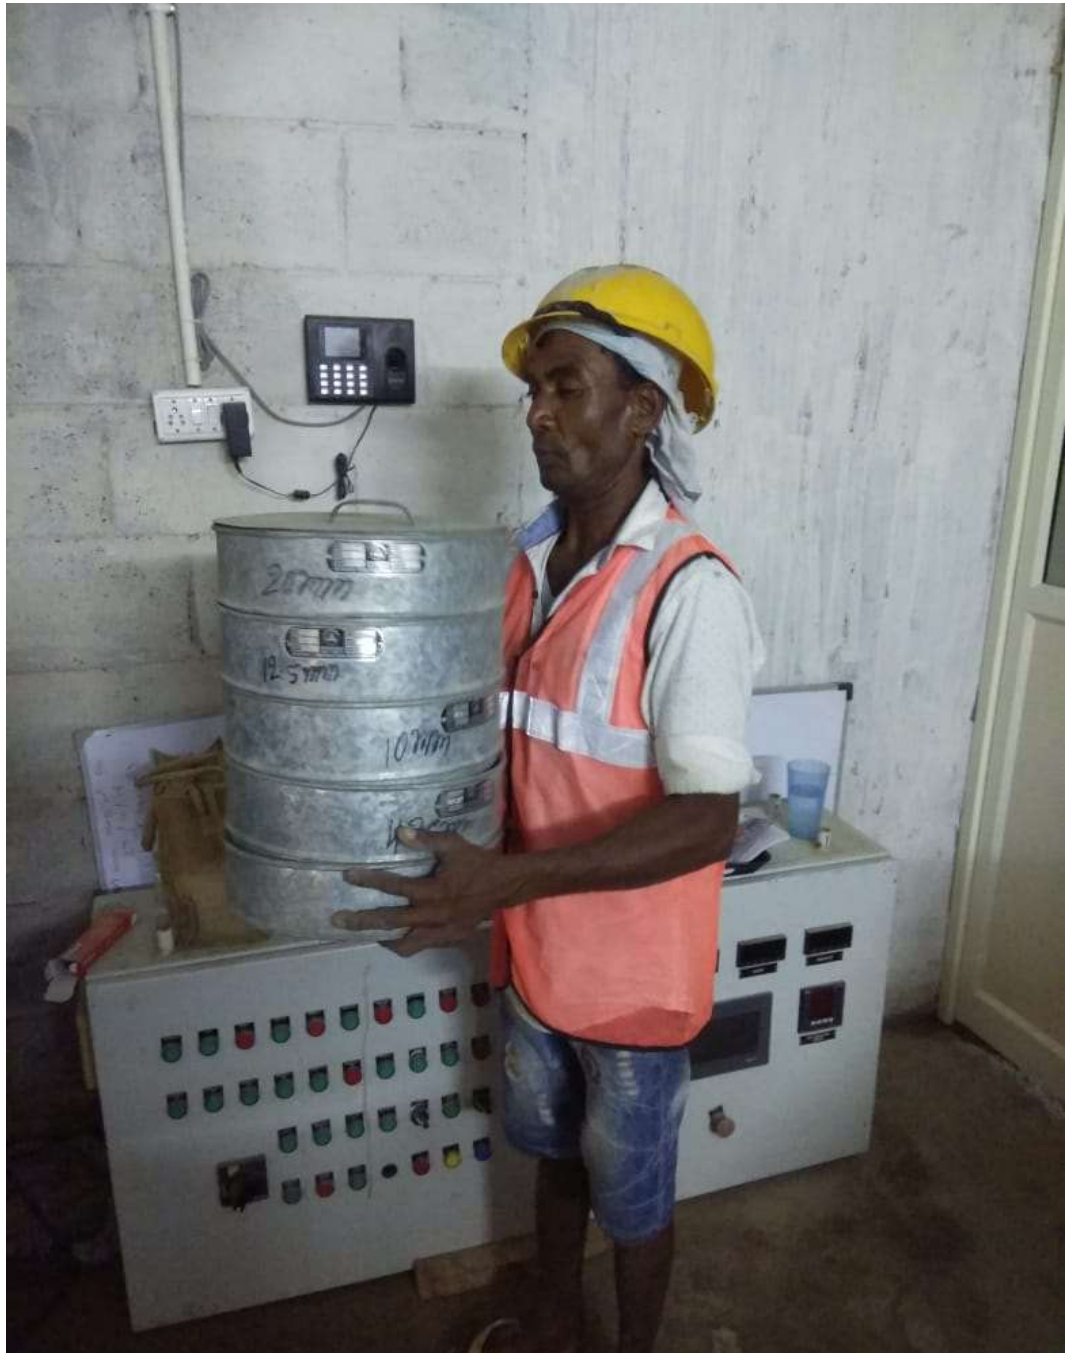

PROGRESS REPORT
CGEWHO – CHENNAI PHASE-III PROJECT

Fine Aggregate Sieve Analysis Testing

