



CENTRAL GOVERNMENT EMPLOYEES WELFARE HOUSING ORGANISATION

CGEWHO Housing Project Phase-III at Kolkata



Monthly Progress Report

Status as on 31/12/2024

NET PROGRESS IN THE MONTH OF DECEMBER'2024 AT CGEWHO HOUSING PROJECT KOLKATA PH-III.

DESCRIPTION	PROGRESS UPTO 30 TH NOVEMBER-2024	PROGRESS UPTO 31 ST DECEMBER-2024
BOUNDARY WALL	◆ 95% Completed except gate, grill and painting.	◆ 95% Completed except gate, grill and painting.
BORE WELL	◆ 02 nos bore well completed.	◆ 02 nos bore well completed.
BLOCK-1 TYPE-C	<ul style="list-style-type: none"> ◆ Anti termite treatment (stage-01)-90% completed. ◆ Anti termite treatment (stage-02)-75% completed ◆ Column and shear wall at stilt floor completed. ◆ Brick Work and earth filling work is 80% Completed up to plinth level. ◆ Shuttering and reinforcement placing work is in progress of Stilt/Ground floor slab. 	<ul style="list-style-type: none"> ◆ Anti termite treatment (stage-01)-90% completed. ◆ Anti termite treatment (stage-02)-90% completed ◆ Brick Work and earth filling work Completed up to plinth level. ◆ 70% of Stilt/Ground floor slab casting completed. ◆ Shuttering and reinforcement placing work is 80%completed and work is in progress for remaining part of Stilt/Ground floor slab in Block-1/Type-C.
BLOCK-2 TYPE-PARKING	Lay out and grid line fixing completed.	Lay out and grid line fixing completed.
BLOCK-3 TYPE-N	<ul style="list-style-type: none"> ◆ Anti termite treatment (stage-1)-95% completed. ◆ Anti termite treatment (stage-2)-90% completed. ◆ Second floor roof slab (part-01) casting completed. ◆ Third floor roof slab (part-01) Mivan shuttering and reinforcement placing work is in progress. ◆ First floor (Part-02) Mivan shuttering and reinforcement placing work 85% completed. ◆ Stilt floor roof slab (part-03) casting completed and Mivan shuttering and reinforcement placing work is progress for first floor. ◆ Brick Work 85% and earth filling work is 30% Completed up to plinth level. 	<ul style="list-style-type: none"> ◆ Anti termite treatment (stage-1)-95% completed. ◆ Anti termite treatment (stage-2)-90% completed. ◆ Third floor roof slab (part-01) casting completed. ◆ Fourth floor roof slab (part-01) Mivan shuttering and reinforcement placing work is in progress. ◆ First floor roof slab (Part-02) casing completed. ◆ Second floor (Part-02) Mivan shuttering and reinforcement placing work is in progress. ◆ First floor Mivan shuttering and reinforcement placing work is in progress. ◆ Brick Work 95% and earth filling work is 30% Completed up to plinth level.
SAMPLE FLAT OF N-TYPE FLAT.	<ul style="list-style-type: none"> ◆ Wall & Ceiling surface preparation & hole packing (almost) completed and Putty work is in progress. ◆ MS grill fixing, Water proofing, Door frame fixing , Plumbing pipe laying & testing works are completed. ◆ Floor tiles and aluminum window fixing works are in progress. 	<ul style="list-style-type: none"> ◆ Putty work is in progress. ◆ Aluminium door window fixing works are completed rectification work is in progress. ◆ Floor tiles fixing work are in progress.
INFRASTRUCTURE/ COMMON AMENITIES		
1. SWIMMING POOL	<ul style="list-style-type: none"> ◆ Foundation Work: Excavation 80% completed. ◆ Pedestal and grade beam 75% completed. 	<ul style="list-style-type: none"> ◆ Foundation Work: Excavation completed. ◆ Pedestal and grade beam 85% completed. ◆ Column up to roof slab 75% completed.

- ◆ Brick Work and earth filling work are Completed up to plinth level in Block-1/Type-C.
- ◆ 70% of Stilt/Ground floor slab casting completed and shuttering work is in progress in Block-1/Type-C.
- ◆ Third floor roof slab (part-01) completed in Block-3/Type-N.
- ◆ Fourth floor roof slab (part-01) Mivan shuttering and reinforcement placing work is in progress in Block-3/Type-N.
- ◆ First floor roof slab (Part-02) casing completed in Block-3/Type-N.
- ◆ Second floor (Part-02) Mivan shuttering and reinforcement placing work is in progress in Block-3/Type-N.
- ◆ First floor (part-03) Mivan shuttering and reinforcement placing work is in progress in Block-3/Type-N.
- ◆ Brick Work 95% and earth filling work is 30% Completed up to plinth level in Block-3/ Type-N.
- ◆ Aluminium door window fixing work are completed in sample flat.
- ◆ Foundation Work for swimming pool: Excavation completed.
- ◆ Pedestal and grade beam for swimming pool : 85% completed.
- ◆ Column up to roof slab 75% completed for swimming pool.




Central Government Employees Welfare Housing Organisation



Block-1/Type-C





Central Government Employees Welfare Housing Organisation



Swimming pool area



Central Government Employees Welfare Housing Organisation

3rd floor roof slab casting (Part-1) of Block-3/Type-N





Central Government Employees Welfare Housing Organisation

4th floor roof slab(Part-1) of Block-3/Type-N





Central Government Employees Welfare Housing Organisation

First floor roof slab casting (Part-2) of Block-3/ Type-N





Central Government Employees Welfare Housing Organisation

Second floor (Part-2)of Block-3/ Type-N



Central Government Employees Welfare Housing Organisation



First floor(Part-3)of Block/3 Type-N





Central Government Employees Welfare Housing Organisation

Block-3/Type-N



PROGRESS REPORT NO-13 , DECEMBER'2024



Central Government Employees Welfare Housing Organisation

Block-3/Type-N





Central Government Employees Welfare Housing Organisation



Curing Work

rMONDAL | 2024.12.30 10:32



Block -1/C-Type




Central Government Employees Welfare Housing Organisation

Curing during casting time.



Flow test of concrete

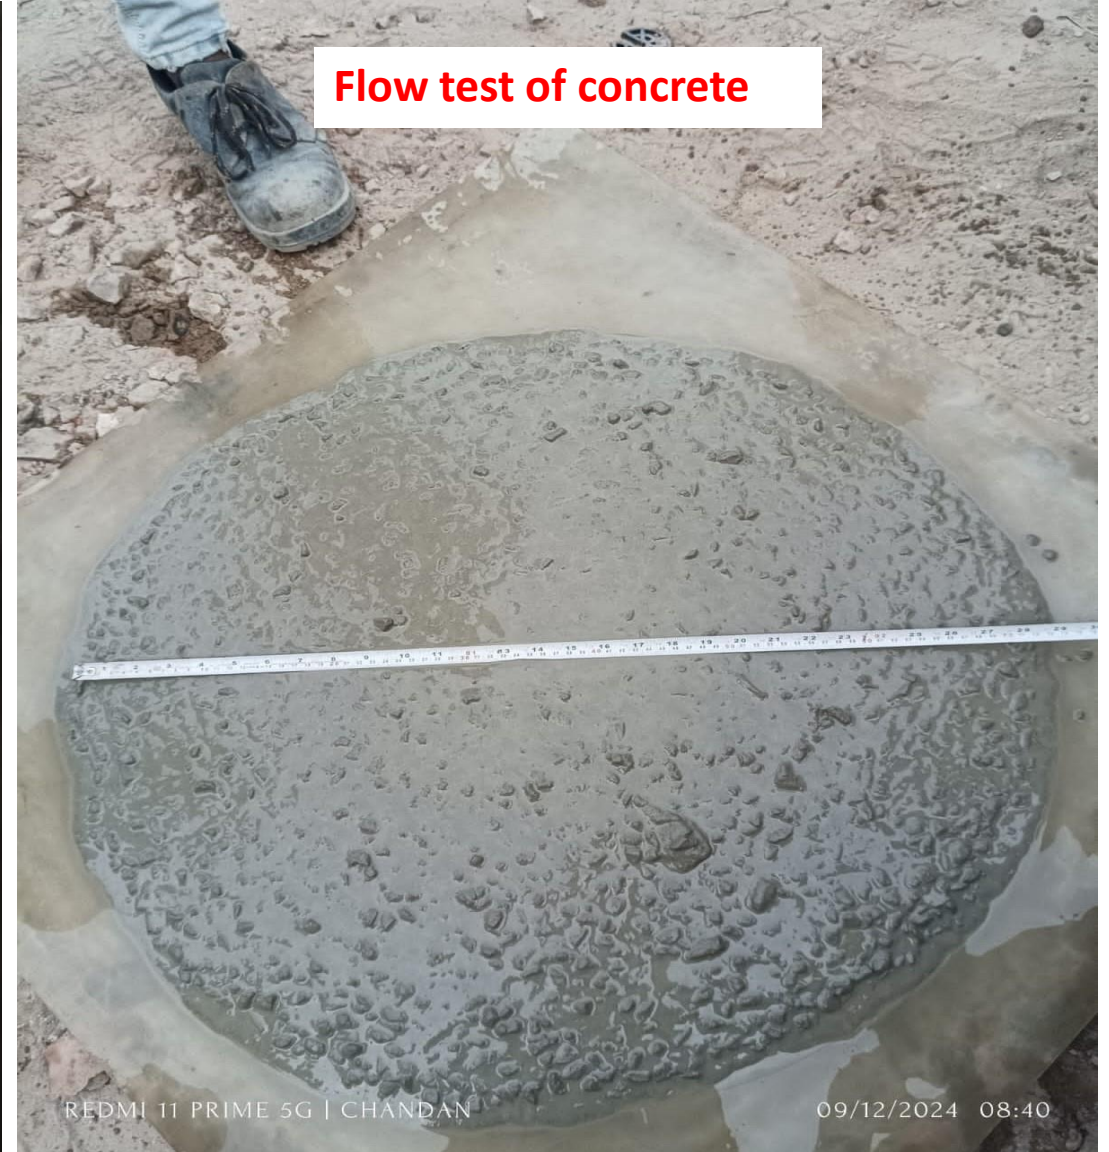

REDMI 11 PRIME 5G | CHANDAN

09/12/2024 08:40
